



Route 17 Gloucester Point Project Update


Marcie Parker
Residency Administrator
August 4, 2009

Schedule

- **Fixed Completion Date – October 31, 2011**
- **Phase 1 Completion – Summer 2010**
- **Phase 2 Completion – Summer 2011**
- **Phase 3 Completion – Fall 2011**

Maintenance of Traffic

- Phase I – 2 lanes each direction with center left turn lane

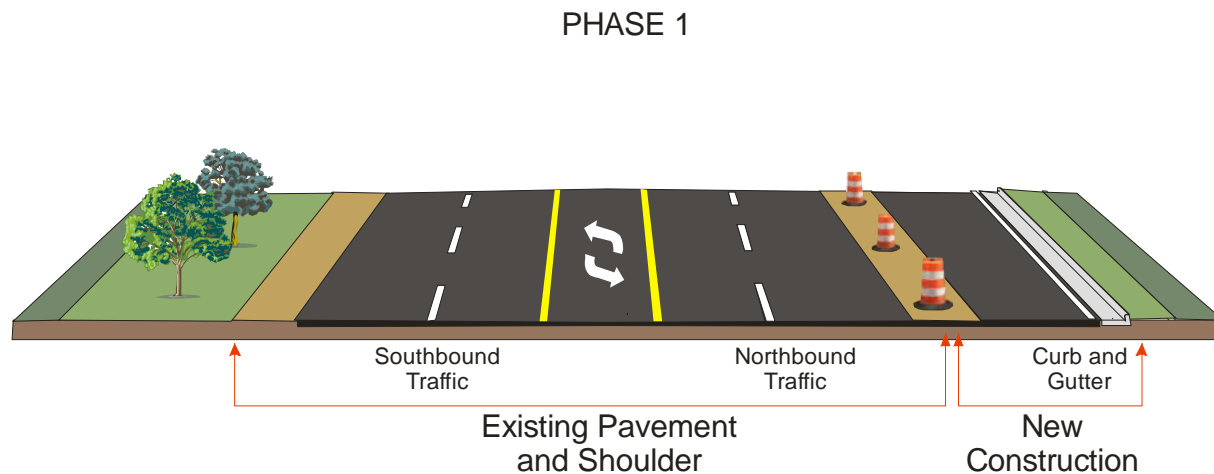

- Daily northbound right lane closures
- Speed Limit is 35 MPH through work zone

Current Activities

- **Water Line Installation**
- **Storm Sewer Installation**
- **Access Road Construction**
- **Temporary Signal Installation completed**

Progress



Storm Sewer Installation over Sanitary Sewer

Progress



Old Asbestos Waterline

Progress



Ductile Iron Pipe to Asbestos Pipe

Progress



Temporary Signalization

30 Day Look Ahead

- **Install Wetland Plants at Stormwater Management Pond**
- **Continue Storm Sewer Installation**
- **Continue Waterline Installation**
- **Continue Access Road Construction**

Questions
