


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Apr	Sep	1st Quarter	Feb	Jul	1st Quarter	Dec	May	Oct	1st Quarter	Mar	Aug	1st Quarter	Jan
1	PROJECT: Tier 1 - Road work w RW & Bridge (PE Only)		726 days	Mon 1/4/21	Fri 12/1/23															
2	Scoping Phase		225 days	Mon 1/4/21	Wed 11/24/21															
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21															
4	22-Scope Project	PM	210 days	Wed 1/27/21	Wed 11/24/21	3														
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21	3FS+10 days														
6	17E-Environmental Review Process (ERP)	ENV	14 days	Thu 2/11/21	Wed 3/3/21	5														
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21	5														
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21	5														
9	21T-Traffic Operations Analysis	TED	40 days	Thu 2/11/21	Thu 4/8/21	5														
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21	5														
11	29X-Public Information Meeting	PM	1 day	Tue 10/26/21	Tue 10/26/21	4FF-20 days														
12	31S-Conduct Location Survey	LDS	110 days	Thu 2/11/21	Mon 7/19/21	5														
13	28-Consultant Procurement	PM	20 days	Fri 3/12/21	Thu 4/8/21	5FS+20 days														
14	36F-Roadway Plan Design / PFI	LD	90 days	Tue 7/13/21	Thu 11/18/21	12FS-5 days														
15	21H-Hydraulic Plan Design / PFI	LDH	30 days	Wed 10/6/21	Thu 11/18/21	14FF														
16	34P-Preliminary Soil Survey	MAT	40 days	Wed 9/22/21	Thu 11/18/21	14FF														
17	36C-PFI Constructability Review	PM	10 days	Thu 10/21/21	Wed 11/3/21	14FF-10 days														
18	24-Determine Permits Needed	ENV	42 days	Thu 3/4/21	Fri 4/30/21	6														
19	36X-PFI Team Meeting Date	PM	1 day	Fri 11/19/21	Fri 11/19/21	13,15,16,17,18,4FF-10 days														
20	Preliminary Design Phase		168 days	Mon 11/22/21	Tue 7/26/22															
21	25-Draft Environmental Document or CE	ENV	85 days	Mon 11/29/21	Fri 4/1/22	4														
22	36H-Hydraulic Plan Design / Public Hearing	LDH	40 days	Mon 11/29/21	Thu 1/27/22	4														
23	36P-Plan Design / Public Hearing	LD	70 days	Mon 11/29/21	Fri 3/11/22	4														
24	30-Preliminary UFI	LDU	35 days	Mon 11/29/21	Thu 1/20/22	4														
25	35-Traffic Control Device Recommendations	LDT	35 days	Mon 11/29/21	Thu 1/20/22	4														
26	37H-River Mechanics Project Studies	LDH	60 days	Mon 11/29/21	Fri 2/25/22	4														
27	37S-Major Structures / Bridge Survey	LDS	85 days	Mon 11/29/21	Fri 4/1/22	4														
28	38-Retaining Wall Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4														
29	39-Sound Wall Foundation Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4														
30	40-Minor Structures Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4														
31	41-Bridge Foundation Data	MAT	40 days	Mon 11/22/21	Mon 1/24/22	37SS														
32	45-Minor Structures Report	MAT	40 days	Mon 12/6/21	Thu 2/3/22	19,30														
33	47X-Willingness Posted Date	PM	1 day	Fri 3/25/22	Fri 3/25/22	34FF-20 days														
34	47-Approve Willingness	PM	30 days	Mon 3/14/22	Fri 4/22/22	23,24														
35	50-Survey Data Verification	LDS	20 days	Fri 2/11/22	Fri 3/11/22	23FS-20 days														
36	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Fri 2/11/22	Fri 3/11/22	23FS-20 days														
37	46B-Preliminary Bridge Plans	SB	90 days	Mon 11/22/21	Tue 4/5/22	19														
38	49C-Design Approval Constructability Review	PM	10 days	Mon 3/14/22	Fri 3/25/22	23,26,29														
39	48-Conduct Location/Design Public Hearing	PM	85 days	Mon 2/28/22	Mon 6/27/22	36FS-10 days,23FS-10 days														
40	48X-Public Hearing Date	PM	1 day	Tue 6/7/22	Tue 6/7/22	39FF-14 days														
41	49-Adopt Location/Design	LD	20 days	Tue 6/28/22	Tue 7/26/22	34,39,38														
42	49X-Location & Design Approval Date	PM	1 day	Tue 7/26/22	Tue 7/26/22	41FF,31														
43	Detailed Design Phase		115 days	Wed 7/27/22	Thu 1/12/23															
44	65F-Plan Design/Field Inspection	LD	85 days	Wed 7/27/22	Tue 11/29/22	32,37,45FF,41														
45	43H-Hydraulic Plan Design / FI	LDH	40 days	Wed 7/27/22	Wed 9/21/22	41														
46	46H-Hydrologic / Hydraulic Analysis / Major Structures	LDH	40 days	Wed 7/27/22	Wed 9/21/22	41														
47	34F-Furnish Final Soils Survey	MAT	85 days	Wed 7/27/22	Tue 11/29/22	41														
48	54-Retaining Wall Data Report	MAT	30 days	Wed 7/27/22	Wed 9/7/22	28,41														
49	55-Noise Abatement Data Report	MAT	30 days	Wed 7/27/22	Wed 9/7/22	41														
50	59-Noise Abatement Design	ENV	85 days	Thu 9/8/22	Thu 1/12/23	49														
51	62-Develop Retaining Structure Plans	SB	65 days	Thu 9/8/22	Tue 12/13/22	48														
52	65C-FI Constructability Review	PM	15 days	Fri 10/21/22	Thu 11/10/22	44FF-10 days														
53	65X-Field Inspection Team Meeting Date	PM	1 day	Wed 11/30/22	Wed 11/30/22	44,46														
54	95-District Closeout Completion Date	PIM	210 days	Wed 2/1/23	Fri 12/1/23	53FS+40 days														

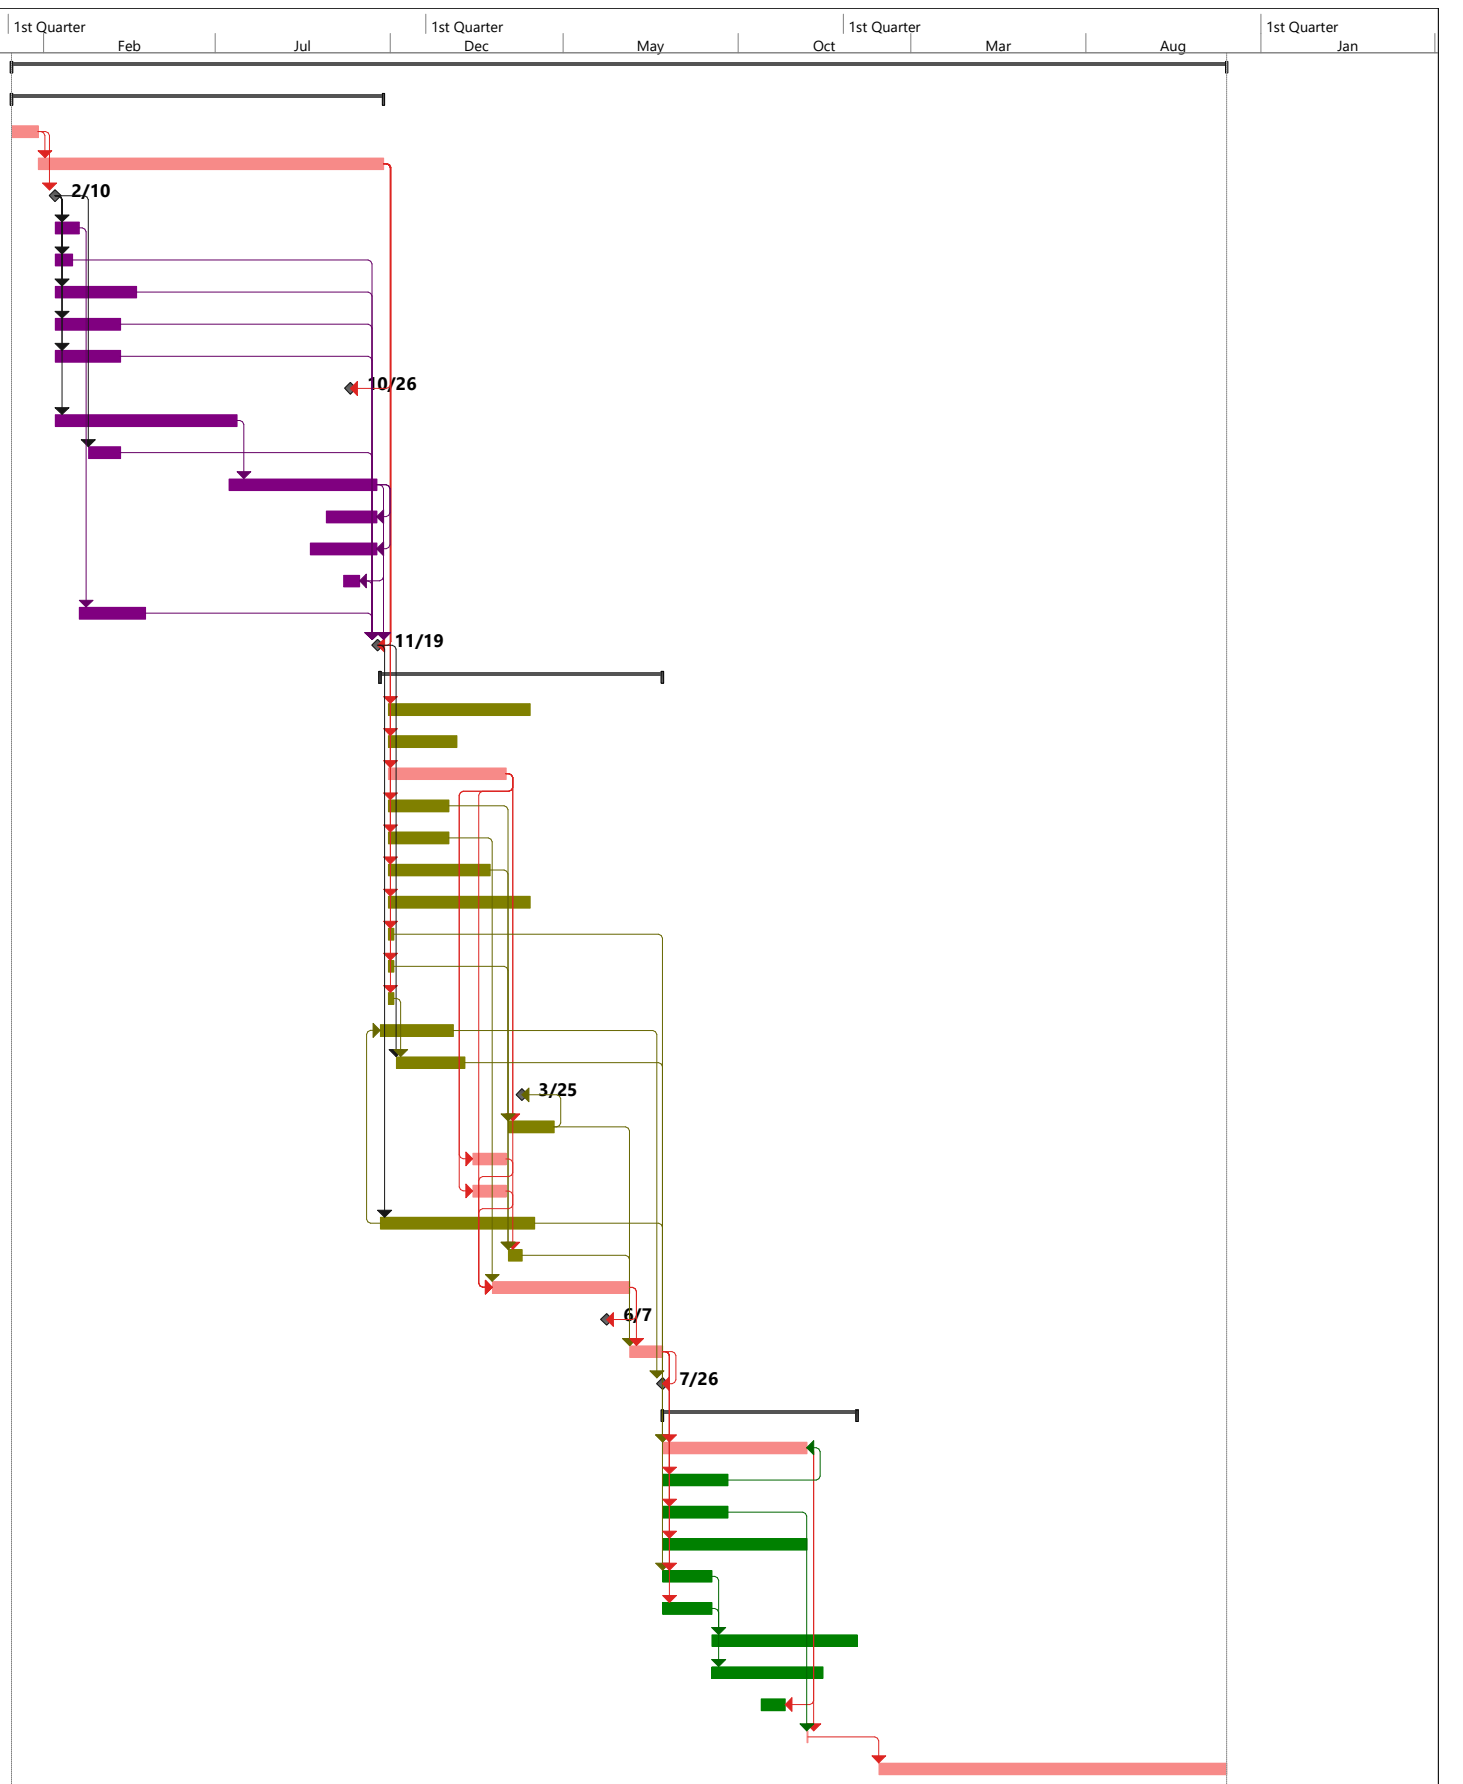

Project: T1_Road_NO_ROW_PE
Date: Thu 2/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
