


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	4th Quarter Sep	Jan	3rd Quarter May	Sep	2nd Quarter Jan	May	Sep	1st Quarter Jan	May	4th Quarter Sep	Jan
1	PROJECT: Tier 1 - Road work w RW (PE Only)		726 days	Mon 1/4/21	Fri 12/1/23													
2	Scoping Phase		225 days	Mon 1/4/21	Wed 11/24/21													
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21		5FS+10 days,4											
4	22-Scope Project	PM	210 days	Wed 1/27/21	Wed 11/24/21		3,4,25,26,27,28,19FF-10 days											
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21		3FS+10 days 6,7,8,9,10,12,13FS+20 days											
6	17E-Environmental Review Process (ERP)	ENV	14 days	Thu 2/11/21	Wed 3/3/21		5	18										
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21		5	19										
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21		5	19										
9	21T-Traffic Operations Analysis	TED	40 days	Thu 2/11/21	Thu 4/8/21		5	19										
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21		5	19										
11	29X-Public Information Meeting	PM	1 day	Tue 10/26/21	Tue 10/26/21		4FF-20 days											
12	31S-Conduct Location Survey	LDS	110 days	Thu 2/11/21	Mon 7/19/21		5	14FS-5 days										
13	28-Consultant Procurement	PM	20 days	Fri 3/12/21	Thu 4/8/21		5FS+20 days	19										
14	36F-Roadway Plan Design / PFI	LD	90 days	Tue 7/13/21	Thu 11/18/21		12FS-5 days	15FF,16FF,17FF-10 days										
15	21H-Hydraulic Plan Design / PFI	LDH	30 days	Wed 10/6/21	Thu 11/18/21		14FF	19										
16	34P-Preliminary Soil Survey	MAT	40 days	Wed 9/22/21	Thu 11/18/21		14FF	19										
17	36C-PFI Constructability Review	PM	10 days	Thu 10/21/21	Wed 11/3/21		14FF-10 days	19										
18	24-Determine Permits Needed	ENV	42 days	Thu 3/4/21	Fri 4/30/21		6	19										
19	36X-PFI Team Meeting Date	PM	1 day	Fri 11/19/21	Fri 11/19/21		13,15,16,17,18,4FF-10 days	29										
20	Preliminary Design Phase		165 days	Mon 11/29/21	Tue 7/26/22													
21	25-Draft Environmental Document or CE	ENV	85 days	Mon 11/29/21	Fri 4/1/22		4											
22	36H-Hydraulic Plan Design / Public Hearing	LDH	40 days	Mon 11/29/21	Thu 1/27/22		4											
23	36P-Plan Design / Public Hearing	LD	70 days	Mon 11/29/21	Fri 3/11/22		4FS-20 days,31,35FS-10 days											
24	30-Preliminary UFI	LDU	35 days	Mon 11/29/21	Thu 1/20/22		4	31										
25	35-Traffic Control Device Recommendations	LDT	35 days	Mon 11/29/21	Thu 1/20/22		4	35FS-10 days										
26	38-Retaining Wall Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21		4	44										
27	39-Sound Wall Foundation Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21		4	34										
28	40-Minor Structures Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21		4	29										
29	45-Minor Structures Report	MAT	40 days	Mon 12/6/21	Thu 2/3/22		19,28	40										
30	47X-Willingness Posted Date	PM	1 day	Fri 3/25/22	Fri 3/25/22		31FF-20 days											
31	47-Approve Willingness	PM	30 days	Mon 3/14/22	Fri 4/22/22		23,24	37,30FF-20 days										
32	50-Survey Data Verification	LDS	20 days	Fri 2/11/22	Fri 3/11/22		23FS-20 days	35FS-10 days										
33	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Fri 2/11/22	Fri 3/11/22		23FS-20 days	35FS-10 days										
34	49C-Design Approval Constructability Review	PM	10 days	Mon 3/14/22	Fri 3/25/22		23,27	37										
35	48-Conduct Location/Design Public Hearing	PM	85 days	Mon 2/28/22	Mon 6/27/22		33FS-10 days,23FS-10 days	37,36FF-14 days										
36	48X-Public Hearing Date	PM	1 day	Tue 6/7/22	Tue 6/7/22		35FF-14 days											
37	49-Adopt Location/Design	LD	20 days	Tue 6/28/22	Tue 7/26/22		31,35,34	38FF,40,41,42,43,44,45										
38	49X-Location & Design Approval Date	PM	1 day	Tue 7/26/22	Tue 7/26/22		37FF											
39	Detailed Design Phase		115 days	Wed 7/27/22	Thu 1/12/23													
40	65F-Plan Design/Field Inspection	LD	85 days	Wed 7/27/22	Tue 11/29/22		29,41FF,37	49,48FF-10 days										
41	43H-Hydraulic Plan Design / FI	LDH	40 days	Wed 7/27/22	Wed 9/21/22		37	40FF										
42	46H-Hydrologic / Hydraulic Analysis / Major Structures	LDH	40 days	Wed 7/27/22	Wed 9/21/22		37	49										
43	34F-Furnish Final Soils Survey	MAT	85 days	Wed 7/27/22	Tue 11/29/22		37											
44	54-Retaining Wall Data Report	MAT	30 days	Wed 7/27/22	Wed 9/7/22		26,37	47										
45	55-Noise Abatement Data Report	MAT	30 days	Wed 7/27/22	Wed 9/7/22		37	46										
46	59-Noise Abatement Design	ENV	85 days	Thu 9/8/22	Thu 1/12/23		45											
47	62-Develop Retaining Structure Plans	SB	65 days	Thu 9/8/22	Tue 12/13/22		44											
48	65C-FI Constructability Review	PM	15 days	Fri 10/21/22	Thu 11/10/22		40FF-10 days											
49	65X-Field Inspection Team Meeting Date	PM	1 day	Wed 11/30/22	Wed 11/30/22		40,42	50FS+40 days										
50	95-District Closeout Completion Date	PIM	210 days	Wed 2/1/23	Fri 12/1/23		49FS+40 days											

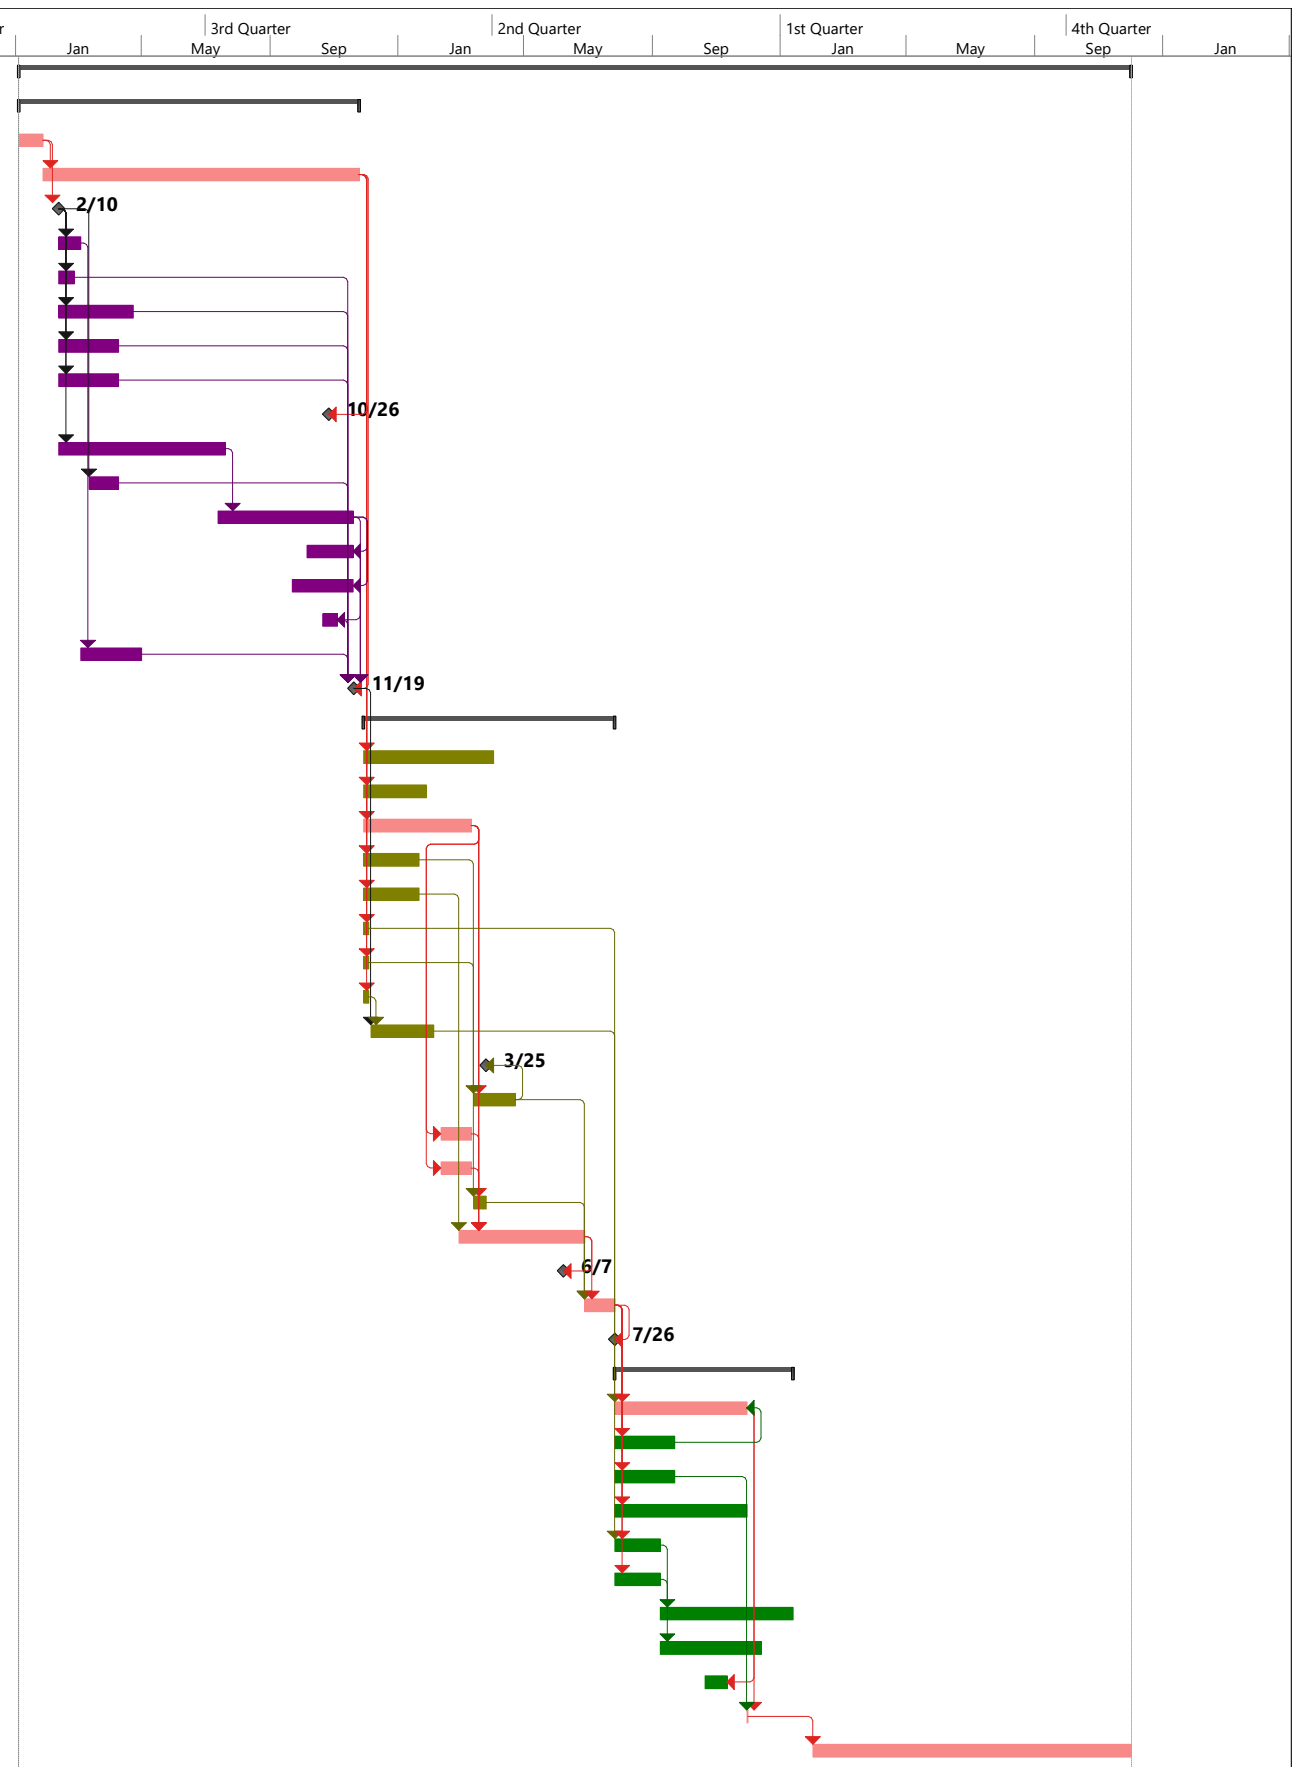

Project: T1_Road_PE
Date: Thu 2/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
