


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	1st Quarter			3rd Quarter			1st Quarter			3rd Quarter		
								Jan	Sep	May	Jan	Sep	May	Jan	Sep	May			
1	<b>PROJECT: Tier 2-Road No Bridge PE Only</b>		<b>1013 days</b>	<b>Mon 1/4/21</b>	<b>Wed 1/29/25</b>														
2	<b>Scoping Phase</b>		<b>315 days</b>	<b>Mon 1/4/21</b>	<b>Fri 4/8/22</b>														
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21		5FS+10 days,4												
4	22-Scope Project	PM	300 days	Wed 1/27/21	Fri 4/8/22		3,7,28,29,19FF-10 days,25,33												
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21		3FS+10 days,6,7,8,9,10,12,13FS+20 days												
6	17E-Environmental Review Process (ERP)	ENV	10 days	Thu 2/11/21	Thu 2/25/21		5	18											
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21		5	19											
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21		5	19											
9	21T-Traffic Operations Analysis	TED	85 days	Thu 2/11/21	Fri 6/11/21		5	19											
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21		5	19											
11	29X-Public Information Meeting	PM	1 day	Fri 3/11/22	Fri 3/11/22		4FF-20 days												
12	31S-Conduct Location Survey	LDS	125 days	Thu 2/11/21	Mon 8/9/21		5	14FS-5 days											
13	28-Consultant Procurement	PM	130 days	Fri 3/12/21	Tue 9/14/21		5FS+20 days	19											
14	36F-Roadway Plan Design / PFI	LD	100 days	Tue 8/3/21	Tue 12/28/21		12FS-5 days	15FF,16FF,17FF-10 days											
15	21H-Hydraulic Plan Design / PFI	LDH	60 days	Wed 9/29/21	Tue 12/28/21		14FF	19											
16	34P-Preliminary Soil Survey	MAT	40 days	Thu 10/28/21	Tue 12/28/21		14FF	19											
17	36C-PFI Constructability Review	PM	14 days	Mon 11/22/21	Mon 12/13/21		14FF-10 days	19											
18	24-Determine Permits Needed	ENV	60 days	Fri 2/26/21	Thu 5/20/21		6	19											
19	36X-PFI Team Meeting Date	PM	1 day	Fri 3/25/22	Fri 3/25/22		13,15,16,17,18,4FF-10 days	30											
20	<b>Preliminary Design Phase</b>		<b>297 days</b>	<b>Mon 4/11/22</b>	<b>Fri 6/16/23</b>														
21	25-Draft Environmental Document or CE	ENV	110 days	Mon 4/11/22	Wed 9/14/22		4	47,48											
22	36H-Hydraulic Plan Design / Public Hearing	LDH	75 days	Mon 4/11/22	Tue 7/26/22		4												
23	36P-Plan Design / Public Hearing	LD	130 days	Mon 4/11/22	Wed 10/12/22		4	31,34,32FS-20 days,35											
24	30-Preliminary UFI	LDU	36 days	Mon 4/11/22	Tue 5/31/22		4												
25	32-Value Engineering	PM	60 days	Mon 4/11/22	Tue 7/5/22		4	38											
26	35-Traffic Control Device Recommendations	LDT	60 days	Mon 4/11/22	Tue 7/5/22		4	35											
27	38-Retaining Wall Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22		4	43											
28	39-Sound Wall Foundation Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22		4	34											
29	40-Minor Structures Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22		4	30											
30	45-Minor Structures Report	MAT	40 days	Mon 4/18/22	Mon 6/13/22		19,29	40											
31	50-Survey Data Verification	LDS	32 days	Thu 10/13/22	Thu 12/1/22		23	35											
32	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Thu 9/15/22	Wed 10/12/22		23FS-20 days	35											
33	53P-Preliminary Landscaping Plans	LDL	45 days	Mon 4/11/22	Mon 6/13/22		4	50											
34	49C-Design Approval Constructability Review	PM	15 days	Thu 10/13/22	Thu 11/3/22		23,28	37											
35	48-Conduct Location/Design Public Hearing	PM	105 days	Fri 12/2/22	Thu 5/4/23		26,31,32,23	37,36FF-14 days											
36	48X-Public Hearing Date	PM	1 day	Fri 4/14/23	Fri 4/14/23		35FF-14 days												
37	49-Adopt Location/Design	LD	30 days	Fri 5/5/23	Fri 6/16/23		35,34	38FF,40,41,42,43,44											
38	49X-Location & Design Approval Date	PM	1 day	Fri 6/16/23	Fri 6/16/23		37FF,25	47,48											
39	<b>Detailed Design Phase</b>		<b>151 days</b>	<b>Mon 6/19/23</b>	<b>Mon 1/29/24</b>														
40	65F-Plan Design/Field Inspection	LD	150 days	Mon 6/19/23	Fri 1/26/24		30,41FF,37	50,49FF-10 days											
41	43H-Hydraulic Plan Design / FI	LDH	85 days	Mon 6/19/23	Wed 10/18/23		37	40FF											
42	34F-Furnish Final Soils Survey	MAT	95 days	Mon 6/19/23	Wed 11/1/23		37												
43	54-Retaining Wall Data Report	MAT	32 days	Mon 6/19/23	Wed 8/2/23		27,37	46											
44	55-Noise Abatement Data Report	MAT	32 days	Mon 6/19/23	Wed 8/2/23		37	45											
45	59-Noise Abatement Design	ENV	100 days	Thu 8/3/23	Thu 12/28/23		44												
46	62-Develop Retaining Structure Plans	SB	85 days	Thu 8/3/23	Wed 12/6/23		43												
47	56-Develop Compensatory Mitigation Design	ENV	150 days	Mon 6/19/23	Fri 1/26/24		21,38												
48	56S-Survey Compensatory Mitigation Site	LDS	150 days	Mon 6/19/23	Fri 1/26/24		21,38												
49	65C-FI Constructability Review	PM	15 days	Tue 12/19/23	Wed 1/10/24		40FF-10 days												
50	65X-Field Inspection Team Meeting Date	PM	1 day	Mon 1/29/24	Mon 1/29/24		40,33	51FS+40 days											
51	95-District Closeout Completion Date	PIM	210 days	Wed 3/27/24	Wed 1/29/25		50FS+40 days												

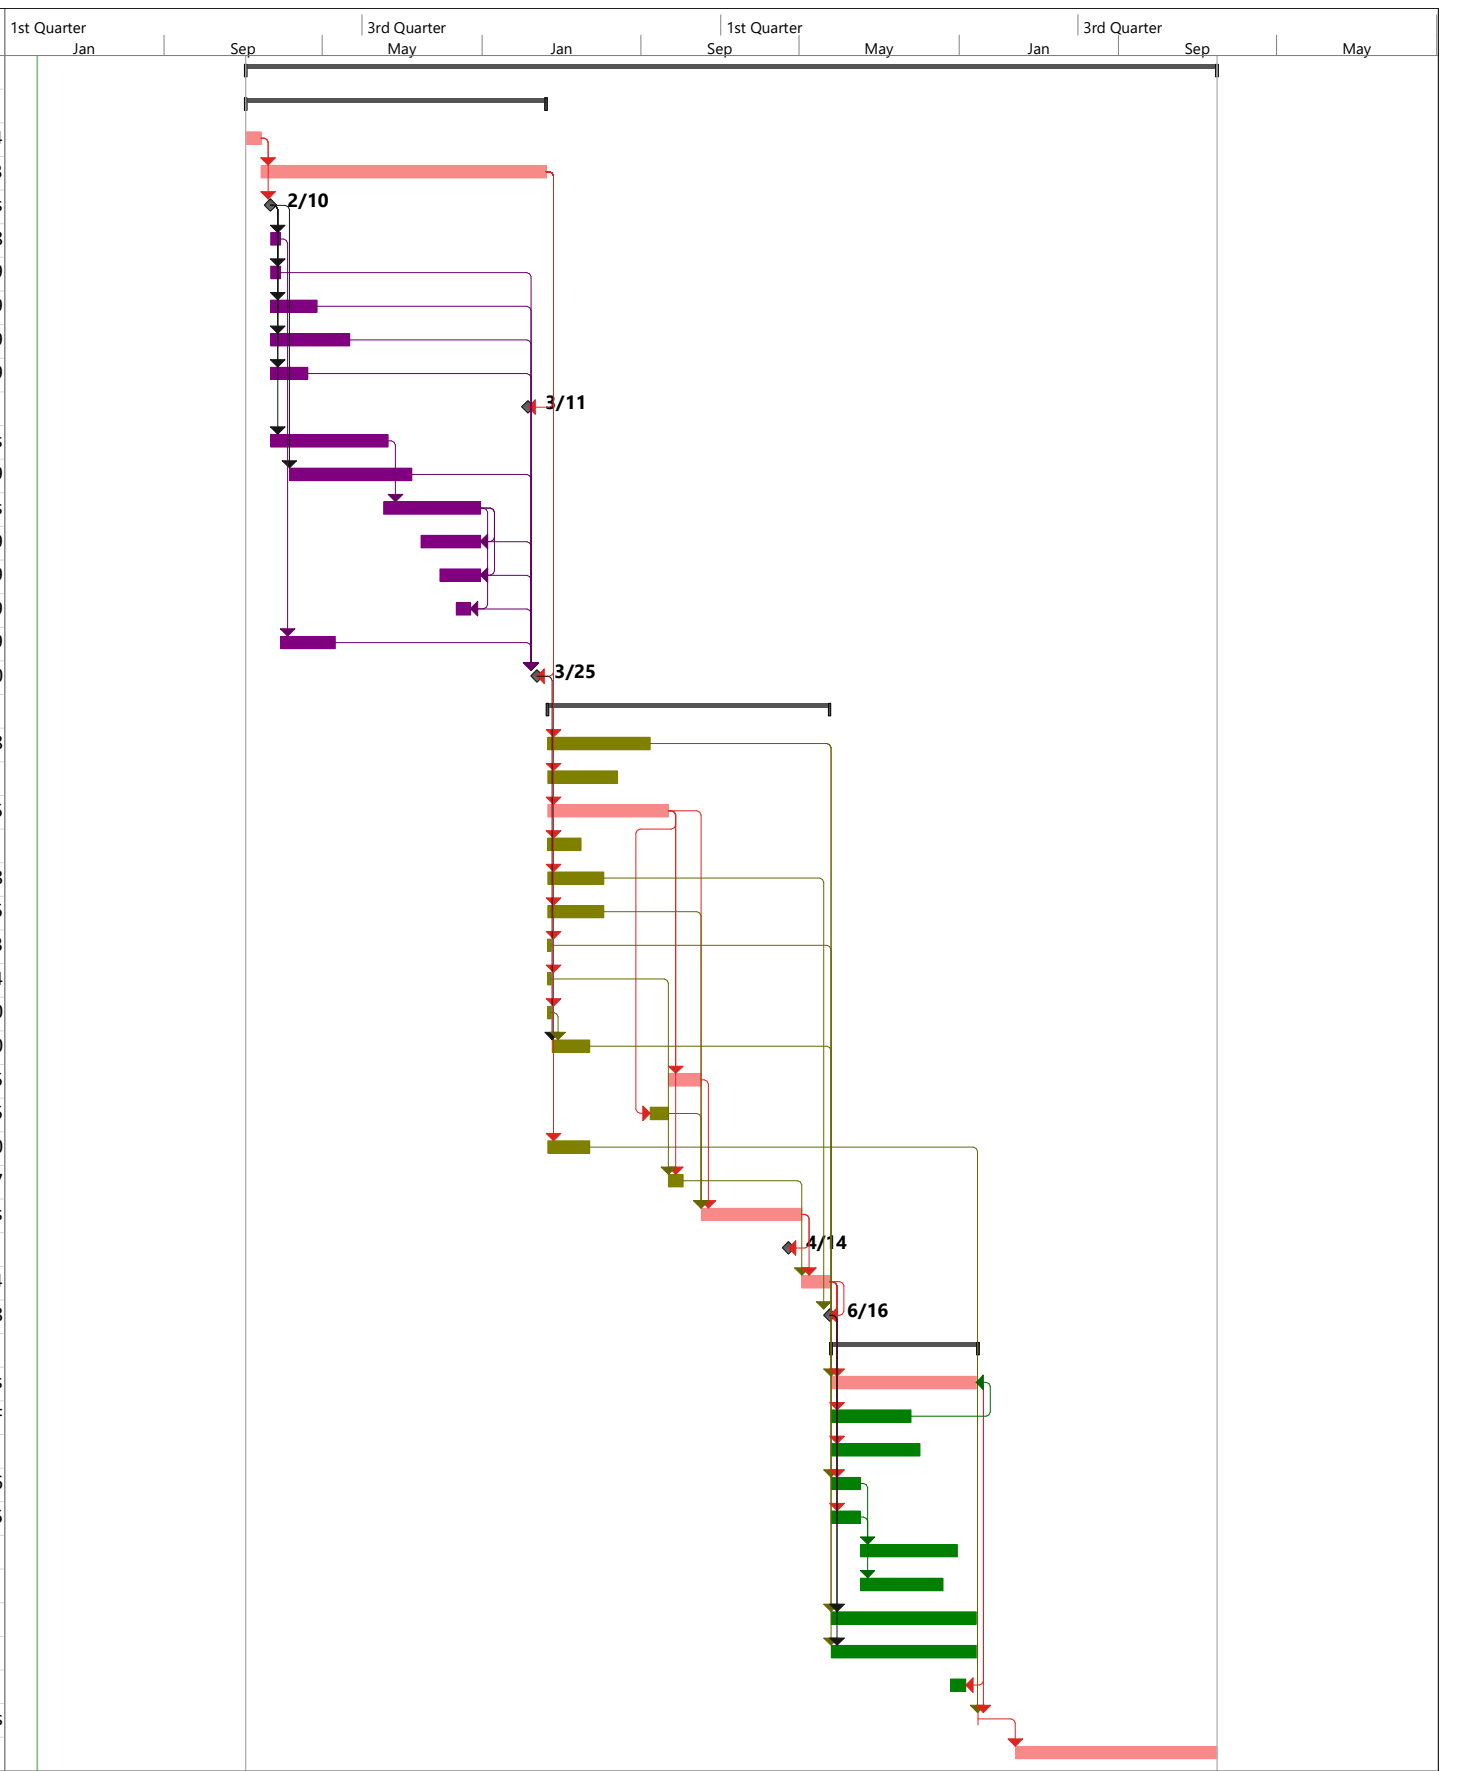

Project: T2\_Road\_PE  
Date: Thu 2/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

Page 1
