


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	er											
								Nov	4th Quarter	3rd Quarter	2nd Quarter	1st Q							
								Nov	Sep	Jul	May	Mar	Jan	Nov	Sep				
1	PROJECT: Study Only		1080 days	Mon 1/4/21	Mon 5/5/25														
2	Scoping Phase		315 days	Mon 1/4/21	Fri 4/8/22														
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21		5FS+10 days,4												
4	22-Scope Project	PM	300 days	Wed 1/27/21	Fri 4/8/22		3 2,23,24,25,19FF-10 days,27												
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21		3FS+10 days 6,7,8,9,10,12,13FS+20 days												
6	17E-Environmental Review Process (ERP)	ENV	10 days	Thu 2/11/21	Thu 2/25/21		5	18											
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21		5	19											
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21		5	19											
9	21T-Traffic Operations Analysis	TED	85 days	Thu 2/11/21	Fri 6/11/21		5	19											
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21		5	19											
11	29X-Public Information Meeting	PM	1 day	Fri 3/11/22	Fri 3/11/22		4FF-20 days												
12	31S-Conduct Location Survey	LDS	125 days	Thu 2/11/21	Mon 8/9/21		5	14FS-5 days											
13	28-Consultant Procurement	PM	130 days	Fri 3/12/21	Tue 9/14/21		5FS+20 days	19											
14	36F-Roadway Plan Design / PFI	LD	100 days	Tue 8/3/21	Tue 12/28/21		12FS-5 days	15FF,16FF,17FF-10 days											
15	21H-Hydraulic Plan Design / PFI	LDH	60 days	Wed 9/29/21	Tue 12/28/21		14FF	19											
16	34P-Preliminary Soil Survey	MAT	40 days	Thu 10/28/21	Tue 12/28/21		14FF	19											
17	36C-PFI Constructability Review	PM	14 days	Mon 11/22/21	Mon 12/13/21		14FF-10 days	19											
18	24-Determine Permits Needed	ENV	60 days	Fri 2/26/21	Thu 5/20/21		6	19											
19	36X-PFI Team Meeting Date	PM	1 day	Fri 3/25/22	Fri 3/25/22		13,15,16,17,18,4FF-10 days												
20	Preliminary Design Phase		265 days	Mon 4/11/22	Tue 5/2/23														
21	25-Draft Environmental Document or CE	ENV	110 days	Mon 4/11/22	Wed 9/14/22		4												
22	36H-Hydraulic Plan Design / Public Hearing	LDH	75 days	Mon 4/11/22	Tue 7/26/22		4												
23	36P-Plan Design / Public Hearing	LD	130 days	Mon 4/11/22	Wed 10/12/22		4	26FS-20 days,28											
24	30-Preliminary UFI	LDU	36 days	Mon 4/11/22	Tue 5/31/22		4												
25	35-Traffic Control Device Recommendations	LDT	60 days	Mon 4/11/22	Tue 7/5/22		4	28											
26	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Thu 9/15/22	Wed 10/12/22		23FS-20 days	28											
27	53P-Preliminary Landscaping Plans	LDL	45 days	Mon 4/11/22	Mon 6/13/22		4												
28	48-Conduct Location/Design Public Hearing	PM	105 days	Thu 10/13/22	Tue 3/21/23		25,26,23	30,29FF-14 days											
29	48X-Public Hearing Date	PM	1 day	Wed 3/1/23	Wed 3/1/23		28FF-14 days												
30	49-Adopt Location/Design	LD	30 days	Wed 3/22/23	Tue 5/2/23		28	31FF,32											
31	49X-Location & Design Approval Date	PM	1 day	Tue 5/2/23	Tue 5/2/23		30FF												
32	33-Final Environmental Document	ENV	250 days	Wed 5/3/23	Thu 5/2/24		30	33FS+40 days											
33	95-District Closeout Completion Date	PIM	210 days	Mon 7/1/24	Mon 5/5/25		32FS+40 days												

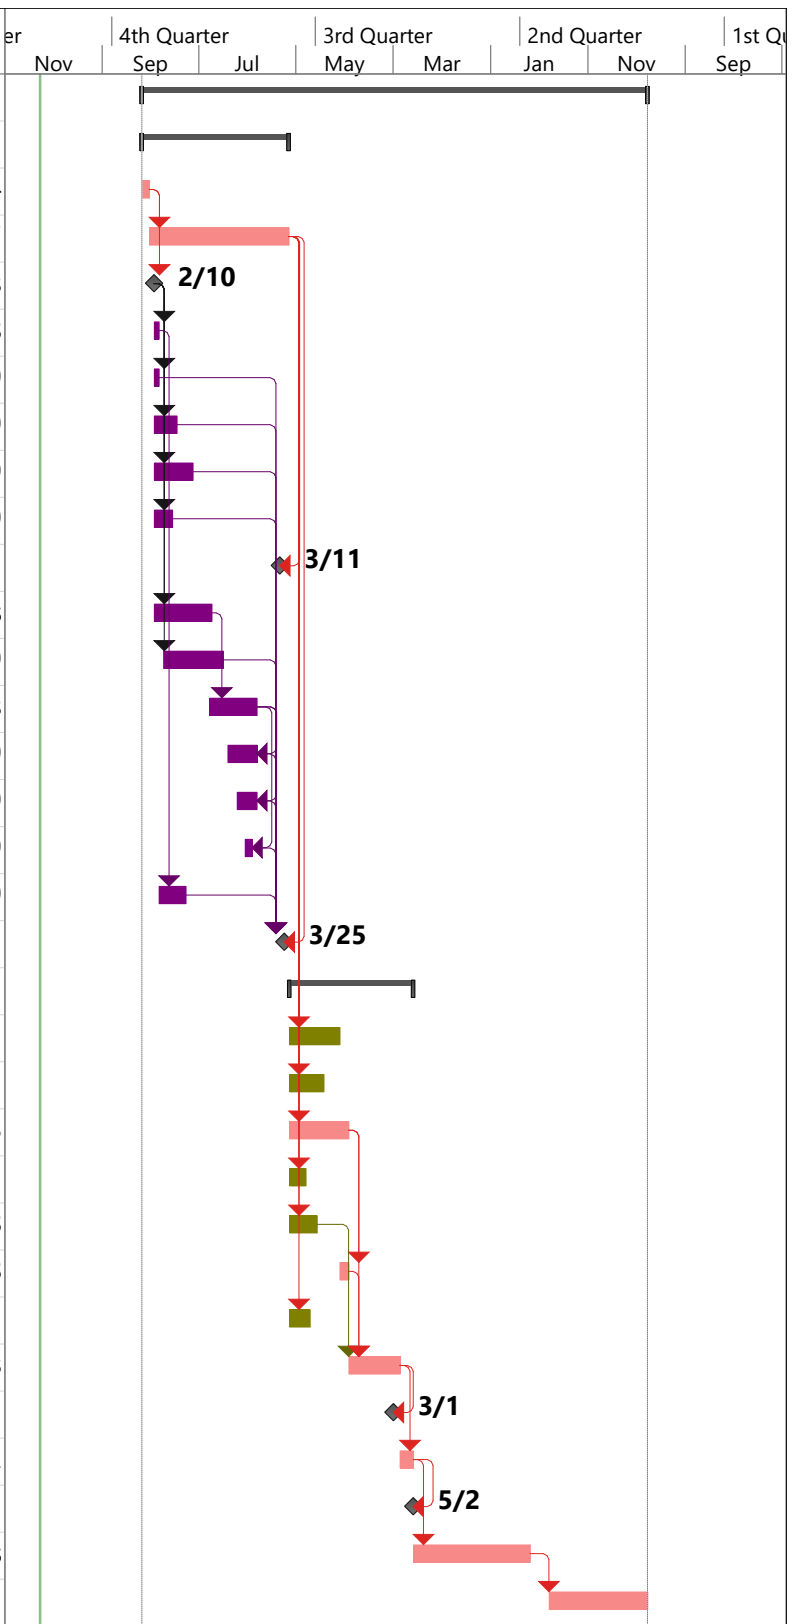

Project: TStudy_PE
Date: Thu 2/20/20

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
