


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors
1	<b>PROJECT: Tier 1-Road with Bridge, no RW</b>		<b>1153 days</b>	<b>Mon 1/4/21</b>	<b>Mon 8/18/25</b>	
2	<b>Scoping Phase</b>		<b>225 days</b>	<b>Mon 1/4/21</b>	<b>Wed 11/24/21</b>	
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21	
4	22-Scope Project	PM	210 days	Wed 1/27/21	Wed 11/24/21	3
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21	3FS+10 days
6	17E-Environmental Review Process (ERP)	ENV	14 days	Thu 2/11/21	Wed 3/3/21	5
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21	5
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21	5
9	21T-Traffic Operations Analysis	TED	40 days	Thu 2/11/21	Thu 4/8/21	5
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21	5
11	29X-Public Information Meeting	PM	1 day	Tue 10/26/21	Tue 10/26/21	4FF-20 days
12	31S-Conduct Location Survey	LDS	110 days	Thu 2/11/21	Mon 7/19/21	5
13	28-Consultant Procurement	PM	20 days	Fri 3/12/21	Thu 4/8/21	5FS+20 days
14	36F-Roadway Plan Design / PFI	LD	90 days	Tue 7/13/21	Thu 11/18/21	12FS-5 days
15	21H-Hydraulic Plan Design / PFI	LDH	30 days	Wed 10/6/21	Thu 11/18/21	14FF
16	34P-Preliminary Soil Survey	MAT	40 days	Wed 9/22/21	Thu 11/18/21	14FF
17	36C-PFI Constructability Review	PM	10 days	Thu 10/21/21	Wed 11/3/21	14FF-10 days
18	24-Determine Permits Needed	ENV	42 days	Thu 3/4/21	Fri 4/30/21	6
19	36X-PFI Team Meeting Date	PM	1 day	Fri 11/19/21	Fri 11/19/21	13,15,16,17,18,4FF-10 days
20	<b>Preliminary Design Phase</b>		<b>123 days</b>	<b>Mon 11/22/21</b>	<b>Fri 5/20/22</b>	
21	25-Draft Environmental Document or CE	ENV	85 days	Mon 11/29/21	Fri 4/1/22	4
22	36H-Hydraulic Plan Design / Public Hearing	LDH	40 days	Mon 11/29/21	Thu 1/27/22	4
23	36P-Plan Design / Public Hearing	LD	70 days	Mon 11/29/21	Fri 3/11/22	4
24	30-Preliminary UFI	LDU	35 days	Mon 11/29/21	Thu 1/20/22	4
25	35-Traffic Control Device Recommendations	LDT	35 days	Mon 11/29/21	Thu 1/20/22	4
26	37H-River Mechanics Project Studies	LDH	60 days	Mon 11/29/21	Fri 2/25/22	4
27	37S-Major Structures / Bridge Survey	LDS	85 days	Mon 11/29/21	Fri 4/1/22	4
28	38-Retaining Wall Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4
29	39-Sound Wall Foundation Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4
30	40-Minor Structures Data Request	LD	5 days	Mon 11/29/21	Fri 12/3/21	4
31	41-Bridge Foundation Data	MAT	40 days	Mon 11/22/21	Mon 1/24/22	37SS
32	45-Minor Structures Report	MAT	40 days	Mon 12/6/21	Thu 2/3/22	19,30
33	47X-Willingness Posted Date	PM	1 day	Fri 3/25/22	Fri 3/25/22	34FF-20 days
34	47-Approve Willingness	PM	30 days	Mon 3/14/22	Fri 4/22/22	23,24
35	50-Survey Data Verification	LDS	20 days	Fri 2/11/22	Fri 3/11/22	23FS-20 days
36	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Fri 2/11/22	Fri 3/11/22	23FS-20 days
37	46B-Preliminary Bridge Plans	SB	90 days	Mon 11/22/21	Tue 4/5/22	19
38	49C-Design Approval Constructability Review	PM	10 days	Mon 3/14/22	Fri 3/25/22	23,26,29
39	49-Adopt Location/Design	LD	20 days	Mon 4/25/22	Fri 5/20/22	34,38
40	49X-Location & Design Approval Date	PM	1 day	Fri 5/20/22	Fri 5/20/22	39FF,31
41	<b>Detailed Design Phase</b>		<b>95 days</b>	<b>Mon 5/23/22</b>	<b>Wed 10/5/22</b>	
42	65F-Plan Design/Field Inspection	LD	85 days	Mon 5/23/22	Wed 9/21/22	32,37,43FF,39
43	43H-Hydraulic Plan Design / FI	LDH	40 days	Mon 5/23/22	Tue 7/19/22	39
44	46H-Hydrologic / Hydraulic Analysis / Major Structures	LDH	40 days	Mon 5/23/22	Tue 7/19/22	39
45	34F-Furnish Final Soils Survey	MAT	85 days	Mon 5/23/22	Wed 9/21/22	39
46	54-Retaining Wall Data Report	MAT	30 days	Mon 5/23/22	Tue 7/5/22	28,39
47	62-Develop Retaining Structure Plans	SB	65 days	Wed 7/6/22	Wed 10/5/22	46
48	65C-FI Constructability Review	PM	15 days	Wed 8/17/22	Wed 9/7/22	42FF-10 days
49	65X-Field Inspection Team Meeting Date	PM	1 day	Thu 9/22/22	Thu 9/22/22	42,44
50	<b>Final Design and ROW Acquisition Phase</b>		<b>181 days</b>	<b>Thu 9/22/22</b>	<b>Thu 6/15/23</b>	
51	64-Final Bridge Plans	SB	160 days	Thu 9/22/22	Tue 5/16/23	42,27
52	65P-Plan Design (PAC)	LD	85 days	Fri 9/23/22	Tue 1/31/23	49
53	51H-Hydraulic Review for Construction / PAC	LDH	30 days	Fri 9/23/22	Fri 11/4/22	49
54	61-Final Traffic Control Device Plans	LDT	85 days	Fri 9/23/22	Tue 1/31/23	25,49
55	46-Review & Approval of ESC and SWM Plan	LDH	10 days	Fri 6/2/23	Thu 6/15/23	57
56	71C-PAC Constructability Review	PM	10 days	Wed 5/17/23	Wed 5/31/23	51,52,54
57	71X-PreAdvertisement Conference (PAC) Date	PM	1 day	Thu 6/1/23	Thu 6/1/23	11,47,52,53,56
58	70-Obtain Environmental Permits	ENV	105 days	Fri 12/16/22	Thu 5/18/23	68FF-60 days
59	70R-Va Stormwater Mgt Program (VSMP) Const Permit	LDH	40 days	Thu 6/1/23	Thu 7/27/23	57SS
60	<b>Advertise Plans Phase</b>		<b>51 days</b>	<b>Fri 6/2/23</b>	<b>Mon 8/14/23</b>	
61	66-Environmental Reevaluation	ENV	10 days	Fri 6/2/23	Thu 6/15/23	57
62	69X-Right of Way / Utility Certification Date	RW	1 day	Mon 8/7/23	Mon 8/7/23	65FF-5 days
63	79-CN Funding Review/Authorization of Funds	PMD	20 days	Fri 6/2/23	Thu 6/29/23	64SS
64	71-Approved CN Plans	PM	27 days	Fri 6/2/23	Tue 7/11/23	57
65	72-Prepare for Advertisement	CN	35 days	Mon 6/26/23	Mon 8/14/23	64SS+16 days
66	72B-Bidability Review	CN	5 days	Mon 7/3/23	Mon 7/10/23	65SS+5 days
67	72X-Plan Submission Date	CN	1 day	Fri 7/28/23	Fri 7/28/23	65FF-11 days
68	<b>80-Advertise Project</b>		<b>1 day</b>	<b>Mon 8/14/23</b>	<b>Mon 8/14/23</b>	<b>65FF,63,62,61</b>
69	<b>Construction</b>		<b>471 days</b>	<b>Wed 9/27/23</b>	<b>Mon 8/18/25</b>	
70	82-Conduct Bid Opening	CN	1 day	Wed 9/27/23	Wed 9/27/23	68FS+30 days
71	84-Award Contract	CN	1 day	Thu 11/2/23	Thu 11/2/23	70FS+24 days
72	91-Administer Contract	PMC	170 days	Wed 12/13/23	Thu 8/15/24	71FS+25 days
73	77S-Construction / Survey	LDS	170 days	Wed 12/13/23	Thu 8/15/24	71FS+25 days
74	88-Survey Monumentation	LDS	40 days	Fri 8/2/24	Fri 9/27/24	72FS-10 days
75	95-District Closeout Completion Date	PIM	210 days	Mon 10/14/24	Mon 8/18/25	72FS+40 days

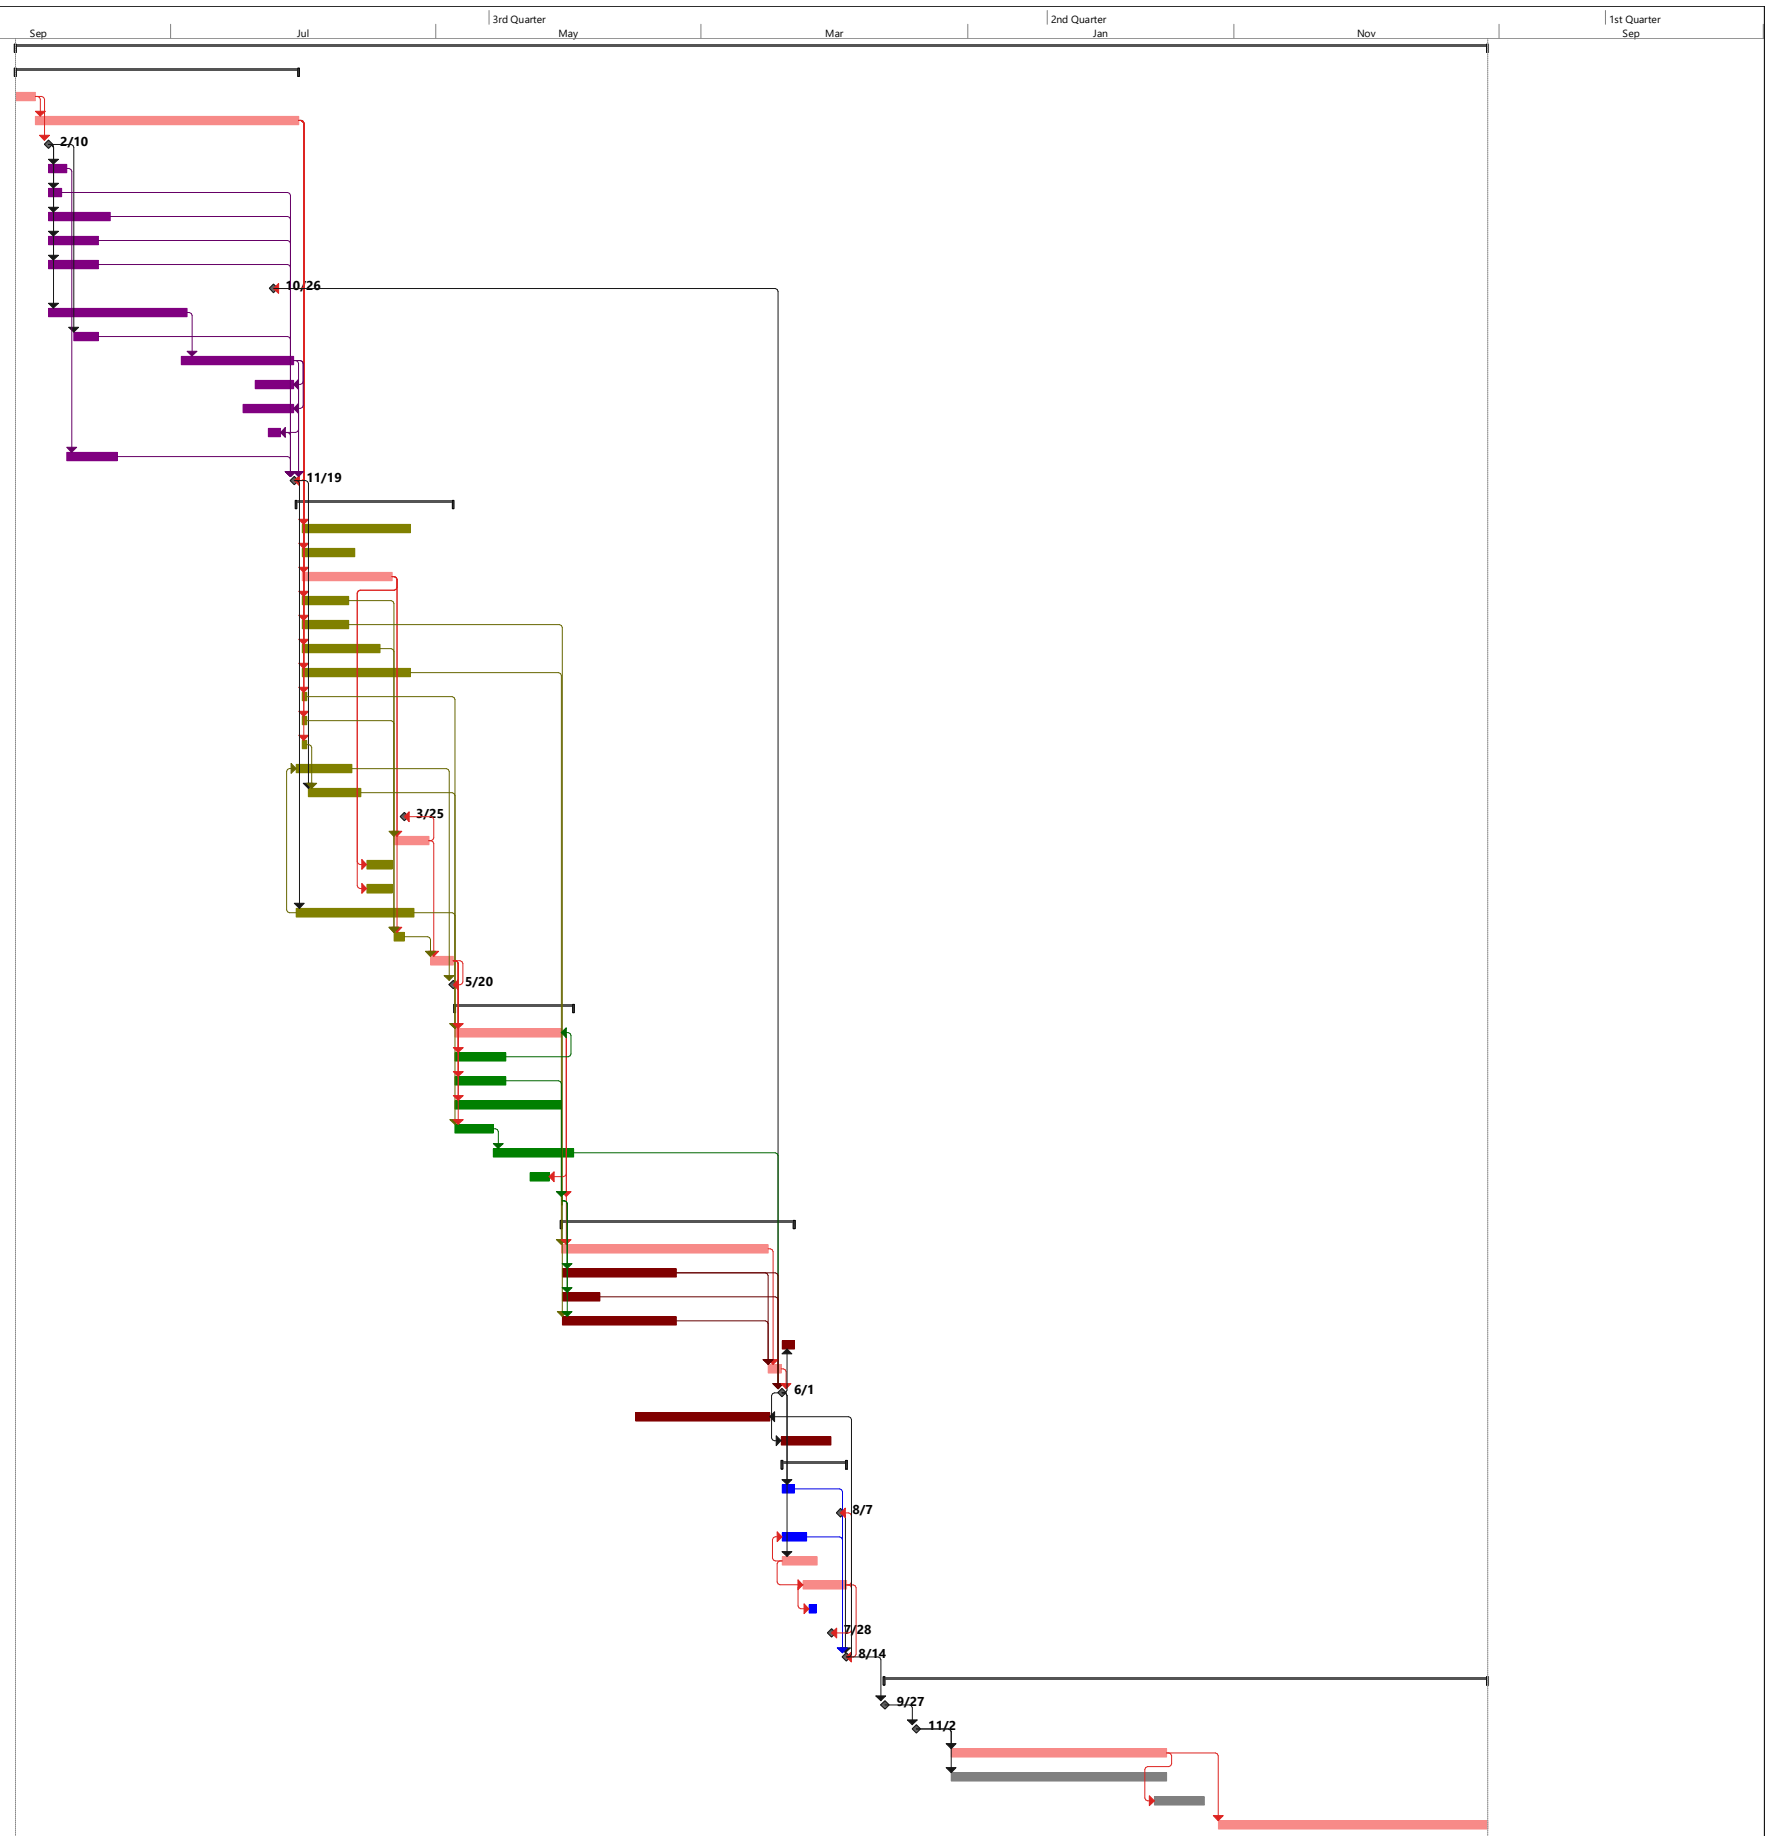

Project: T1\_Road\_BR\_PE\_UT\_CN  
Date: Thu 2/20/20

Task Milestone Project Summary Inactive Milestone Manual Task Manual Summary Rollup Start-only External Tasks Deadline Critical Split Manual Progress

Split Summary Inactive Task Inactive Summary Duration-only Manual Summary Finish-only External Milestone Critical Progress

Page 1
