


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	y	January	July	January	July	Ja				
							12/16	9/8	5/31	2/21	11/14	8/7	4/30	1/21	10/13	7/6
1	<b>PROJECT: DRPT - Equipment</b>		<b>1024 days</b>	<b>Mon 1/4/21</b>	<b>Thu 2/13/25</b>											
2	110-Grant Award	PMD	80 days	Mon 1/4/21	Mon 5/3/21											
3	112-Authorize DRPT Funds	PM	10 days	Tue 5/4/21	Mon 5/17/21	2										
4	122-Scope DRPT Project	PM	5 days	Tue 5/18/21	Mon 5/24/21	3										
5	180-RFP/Advertisement	PM	60 days	Tue 5/25/21	Fri 8/20/21	4										
6	184-Procurement/Vendor Award	PM	120 days	Mon 8/23/21	Thu 3/3/22	5										
7	191-Delivery/Testing & Acceptance	PM	375 days	Fri 3/4/22	Thu 9/21/23	6										
8	195-Start Operations	PM	90 days	Fri 9/22/23	Tue 2/13/24	7										
9	95-District Closeout Completion Date	PIM	210 days	Thu 4/11/24	Thu 2/13/25	8FS+40 days										

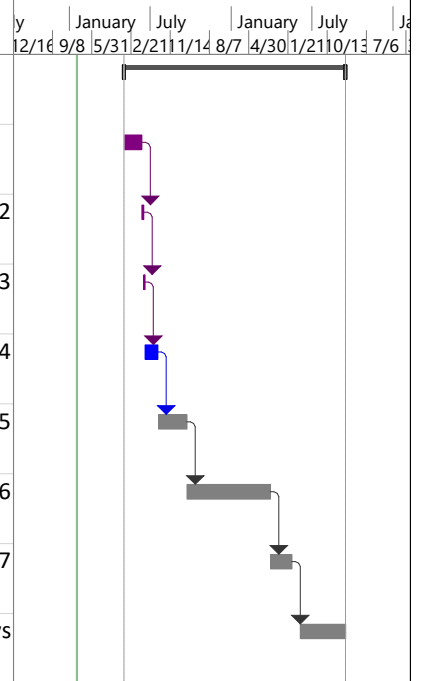

Project: DRPT_Equipment Date: Thu 2/20/20	Task		Inactive Task		Manual Summary Rollup		External Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline	
	Milestone		Inactive Summary		Start-only		Progress	
	Summary		Manual Task		Finish-only		Manual Progress	
	Project Summary		Duration-only		External Tasks			
