


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	October	May	December	July	February	September
1	PROJECT: LAP Tier 1 CN Only		776 days	Mon 1/4/21	Thu 2/15/24			B	M	E	B	M	E
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21		3						
3	22-Scope Project	PM	10 days	Thu 5/13/21	Wed 5/26/21	2	4						
4	72-Prepare for Advertisement	CN	65 days	Thu 5/27/21	Fri 8/27/21	3	7SS,6SS,8						
5	70-Obtain Environmental Permits	ENV	105 days	Wed 2/3/21	Thu 7/1/21	8FF-60 days							
6	69X-Right of Way / Utility Certification Date	RW	10 days	Thu 5/27/21	Thu 6/10/21	4SS	8						
7	79-CN Funding Review/Authorization of Funds	PMD	20 days	Thu 5/27/21	Thu 6/24/21	4SS	8						
8	80-Advertise Project	CN	20 days	Mon 8/30/21	Mon 9/27/21	7,6,4	9FS+55 days,5FF-60 days						
9	84-Award Contract	CN	1 day	Mon 12/20/21	Mon 12/20/21	8FS+55 days	10FS+25 days						
10	91-Administer Contract	PMC	260 days	Mon 1/31/22	Tue 2/14/23	9FS+25 days	11FS+40 days						
11	95-District Closeout Completion Date	PIM	210 days	Thu 4/13/23	Thu 2/15/24	10FS+40 days							

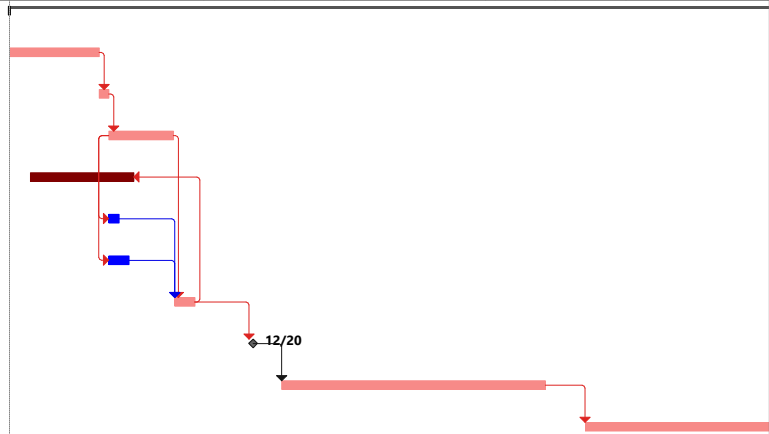

Project: LAP1_CN
Date: Wed 2/12/20

Task	Summary	Inactive Milestone	External Milestone	Duration-only	Start-only	Critical Split
Split	Project Summary	Inactive Summary	Deadline	Manual Summary Rollup	Finish-only	Progress
Milestone	Inactive Task	Manual Task	Critical	Manual Summary	External Tasks	Manual Progress
