


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	
1	PROJECT: LAP Study Only		890 days	Mon 1/4/21	Mon 7/29/24			
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21			3
3	12-Authorize Preliminary Engineering	PMD	15 days	Thu 5/13/21	Thu 6/3/21	2		4,5
4	17E-Environmental Review Process (ERP)	ENV	75 days	Fri 6/4/21	Mon 9/20/21	3		8
5	28-Consultant Procurement	PM	130 days	Fri 6/4/21	Fri 12/10/21	3		6
6	22-Scope Project	PM	80 days	Mon 12/13/21	Fri 4/8/22	5		7
7	65F-Plan Design/Field Inspection	LD	325 days	Mon 4/11/22	Thu 7/27/23	6	9FS+40 days	
8	25-Draft Environmental Document or CE	ENV	85 days	Tue 9/21/21	Thu 1/27/22	4	9FS+40 days	
9	95-District Closeout Completion Date	PIM	210 days	Mon 9/25/23	Mon 7/29/24	8FS+40 days,7FS+40 days		

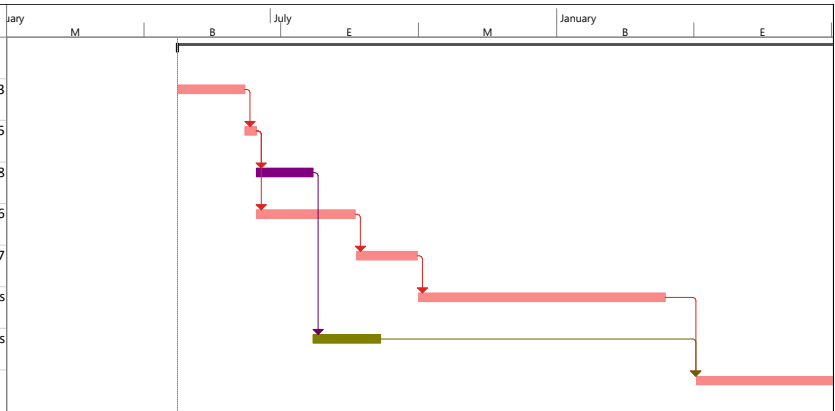

Project: LAP_Study_Only
Date: Wed 2/12/20

Task	Summary	Inactive Milestone	External Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress	Critical Split
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress	Critical Split

Page 1
