


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	January 1 3/1	September 6/28	May 1 10/25	January 1 6/20	September 12/13	May 1 10/9	September 2/5
1	PROJECT: Paving Plant Mix		458 days	Mon 1/4/21	Tue 11/1/22								
2	22-Scope Project	PM	5 days	Mon 1/4/21	Fri 1/8/21								
3	17E-Environmental Review Process (ERP)	ENV	10 days	Mon 1/4/21	Tue 1/19/21								
4	25-Draft Environmental Document or CE	ENV	10 days	Mon 1/4/21	Tue 1/19/21								
5	25-Draft Environmental Document or CE	ENV	10 days	Mon 1/4/21	Tue 1/19/21								
6	66-Environmental Reevaluation	ENV	5 days	Mon 1/4/21	Fri 1/8/21								
7	69X-Right of Way / Utility Certification Date	RW	1 day	Mon 1/4/21	Mon 1/4/21								
8	80-Advertise Project	CN	1 day	Mon 1/11/21	Mon 1/11/21	2							
9	82-Conduct Bid Opening	CN	1 day	Fri 2/26/21	Fri 2/26/21	8FS+30 days							
10	84-Award Contract	CN	1 day	Mon 4/5/21	Mon 4/5/21	9FS+25 days							
11	91-Administer Contract	PMC	120 days	Tue 5/11/21	Fri 10/29/21	10FS+25 days							
12	95-District Closeout Completion Date	PIM	210 days	Mon 1/3/22	Tue 11/1/22	11FS+40 days							

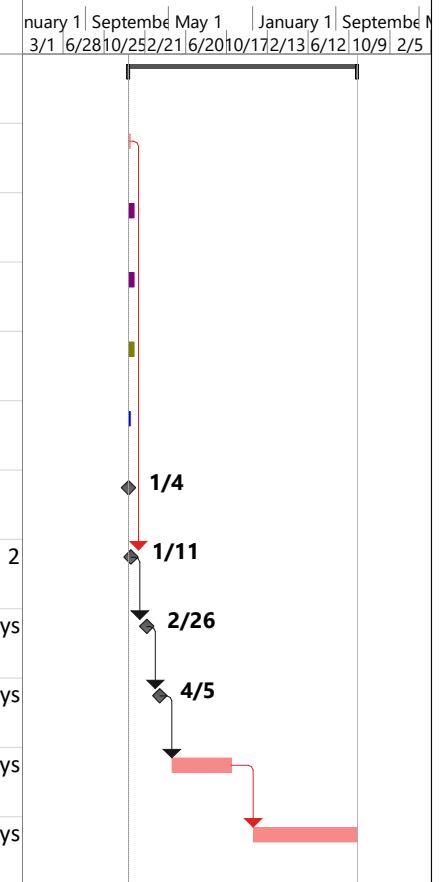

Project: Pavement_Plant_Mix Date: Thu 2/20/20	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Progress	
	Milestone		Manual Task		External Tasks		Manual Progress	
	Summary		Duration-only		External Milestone			
	Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical				
