


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	November 21		December 11		January 1		January 21		Feb
							9/15	3/22	9/27	4/4	10/10	4/17	10/23	4/30	11/5
1	PROJECT: Tier 1 - Complex Maintenance (PE & CN)		681 days	Mon 1/4/21	Mon 9/25/23										
2	12-Authorize Preliminary Engineering	PMD	10 days	Mon 1/4/21	Tue 1/19/21										
3	22-Scope Project	PM	50 days	Wed 1/20/21	Wed 3/31/21	2									
4	22X-Scoping Team Meeting Date	PM	1 day	Wed 1/27/21	Wed 1/27/21	3SS+5 days									
5	17E-Environmental Review Process (ERP)	ENV	5 days	Thu 4/1/21	Wed 4/7/21	3									
6	24-Determine Permits Needed	ENV	40 days	Thu 4/8/21	Thu 6/3/21	5									
7	25-Draft Environmental Document or CE	ENV	40 days	Fri 6/4/21	Fri 7/30/21	6									
8	65F-Plan Design/Field Inspection	LD	40 days	Thu 4/1/21	Wed 5/26/21	3,4									
9	43-Furnish Utility Field Inspection Plans	LD	5 days	Thu 5/27/21	Thu 6/3/21	8									
10	43X-Utility Field Inspection Team Meeting Date	PM	1 day	Fri 6/4/21	Fri 6/4/21	9									
11	51X-Right of Way and Utilities Plan Date	PM	1 day	Mon 6/7/21	Mon 6/7/21	10									
12	52-Authorize RW & UT Funds	PMD	10 days	Tue 6/8/21	Mon 6/21/21	11									
13	67U-Utility Relocation By Others	RW	90 days	Tue 6/22/21	Thu 10/28/21	12									
14	51H-Hydraulic Review for Construction / PAC	LDH	40 days	Thu 5/27/21	Fri 7/23/21	8									
15	65P-Plan Design (PAC)	LD	60 days	Mon 6/7/21	Mon 8/30/21	10									
16	70R-Va Stormwater Mgt Program (VSMP) Const P	LDH	40 days	Tue 8/17/21	Tue 10/12/21	15FS-10 days									
17	46-Review & Approval of ESC and SWM Plan	LDH	10 days	Thu 5/27/21	Thu 6/10/21	8									
18	70-Obtain Environmental Permits	ENV	40 days	Fri 6/4/21	Fri 7/30/21	6									
19	71C-PAC Constructability Review	PM	10 days	Thu 5/27/21	Thu 6/10/21	8									
20	71X-PreAdvertisement Conference (PAC) Date	PM	0 days	Tue 10/12/21	Tue 10/12/21	8,14,16,17,19									
21	66-Environmental Reevaluation	ENV	5 days	Wed 10/13/21	Wed 10/20/21	18,20,7									
22	72-Prepare for Advertisement	CN	22 days	Wed 10/13/21	Mon 11/15/21	20									
23	72B-Bidability Review	CN	5 days	Mon 10/25/21	Fri 10/29/21	22FF-10 days									
24	72X-Plan Submission Date	CN	1 day	Thu 10/28/21	Thu 10/28/21	22FF-11 days									
25	69X-Right of Way / Utility Certification Date	RW	1 day	Fri 11/5/21	Fri 11/5/21	22FF-5 days									
26	80-Advertise Project	CN	1 day	Tue 11/16/21	Tue 11/16/21	22,25,21,13									
27	82-Conduct Bid Opening	CN	1 day	Tue 1/4/22	Tue 1/4/22	26FS+30 days									
28	84-Award Contract	CN	1 day	Fri 2/11/22	Fri 2/11/22	27FS+25 days									
29	91-Administer Contract	PMC	130 days	Tue 3/22/22	Thu 9/22/22	28FS+25 days									
30	95-District Closeout Completion Date	PIM	210 days	Tue 11/22/22	Mon 9/25/23	29FS+40 days									

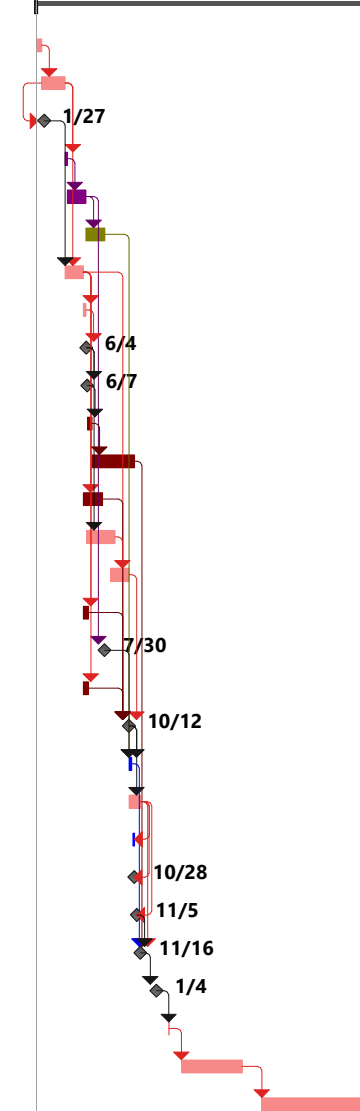

Project: T1_Maint_Complex_PE_ Date: Thu 2/20/20

Task		Inactive Milestone		Start-only		Critical Split	
Split		Inactive Summary		Finish-only		Progress	
Milestone		Manual Task		External Tasks		Manual Progress	
Summary		Duration-only		External Milestone			
Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical			
