


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	er 1 June 1	January 2	September	May 1					
							3/8	6/28	10/18	2/7	5/30	9/19	1/9	5/1	8/21
1	PROJECT: State forces/Hired equip CN Only		396 days	Mon 1/4/21	Wed 8/3/22										
2	22-Scope Project	PM	20 days	Mon 1/4/21	Tue 2/2/21										
3	17E-Environmental Review Process (ERP)	ENV	10 days	Tue 1/5/21	Wed 1/20/21	2SS+1 day									
4	24-Determine Permits Needed	ENV	15 days	Thu 1/21/21	Wed 2/10/21	3									
5	65F-Plan Design/Field Inspection	LD	40 days	Wed 2/3/21	Wed 3/31/21	2									
6	70R-Va Stormwater Mgt Program (VSMP) Const P	LDH	40 days	Wed 2/3/21	Wed 3/31/21	2									
7	46-Review & Approval of ESC and SWM Plan	LDH	10 days	Thu 3/18/21	Wed 3/31/21	5FF,2									
8	66-Environmental Reevaluation	ENV	5 days	Thu 2/11/21	Wed 2/17/21	4									
9	79-CN Funding Review/Authorization of Funds	PMD	10 days	Thu 3/18/21	Wed 3/31/21	5FF									
10	80-Advertise Project	CN	1 day	Thu 4/1/21	Thu 4/1/21	9,6,5,4,8									
11	81-State Forces/Hired Equipment or Railroad Forc	PM	85 days	Fri 4/2/21	Mon 8/2/21	10									
12	95-District Closeout Completion Date	PIM	210 days	Wed 9/29/21	Wed 8/3/22	11FS+40 days									

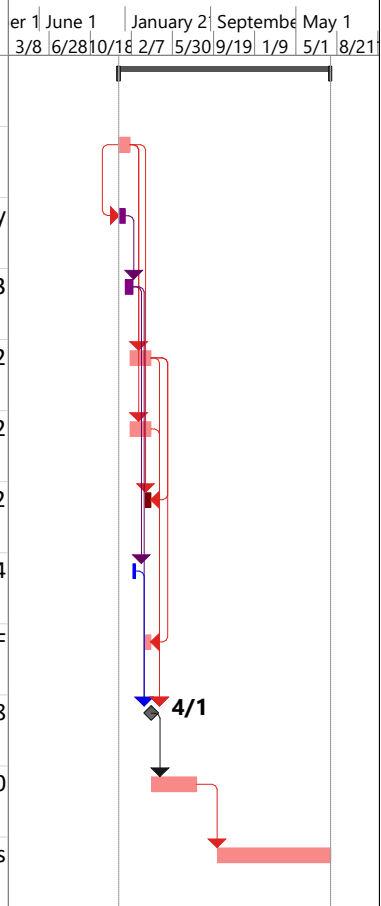

Project: T1_State_Force_Hired_E Date: Thu 2/20/20	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Progress	
	Milestone		Manual Task		External Tasks		Manual Progress	
	Summary		Duration-only		External Milestone			
	Project Summary		Manual Summary Rollup		Deadline			
	Inactive Task		Manual Summary		Critical			
