


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	1st Quarter	3rd Quarter	1st Quarter	3rd Quarter		
								Jan	Sep	May	Jan	Sep	May
1	PROJECT: Tier 2 - Road work w RW, Bridge (PE Only)		1013 days	Mon 1/4/21	Wed 1/29/25								
2	Scoping Phase		315 days	Mon 1/4/21	Fri 4/8/22								
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21		5FS+10 days,4						
4	22-Scope Project	PM	300 days	Wed 1/27/21	Fri 4/8/22		39,30,31,19FF-10 days,25,37						
5	22X-Scoping Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21		3FS+10 days 6,7,8,9,10,12,13FS+20 days						
6	17E-Environmental Review Process (ERP)	ENV	10 days	Thu 2/11/21	Thu 2/25/21	5	18						
7	22C-Scoping Constructability Review	PM	10 days	Thu 2/11/21	Thu 2/25/21	5	19						
8	22S-Photogrammetry/Aerial Photo/Image Processing	LDS	50 days	Thu 2/11/21	Thu 4/22/21	5	19						
9	21T-Traffic Operations Analysis	TED	85 days	Thu 2/11/21	Fri 6/11/21	5	19						
10	23-Furnish Environmental Traffic Data	TMP	40 days	Thu 2/11/21	Thu 4/8/21	5	19						
11	29X-Public Information Meeting	PM	1 day	Fri 3/11/22	Fri 3/11/22	4FF-20 days							
12	31S-Conduct Location Survey	LDS	125 days	Thu 2/11/21	Mon 8/9/21	5	14FS-5 days						
13	28-Consultant Procurement	PM	130 days	Fri 3/12/21	Tue 9/14/21	5FS+20 days	19						
14	36F-Roadway Plan Design / PFI	LD	100 days	Tue 8/3/21	Tue 12/28/21	12FS-5 days	15FF,16FF,17FF-10 days						
15	21H-Hydraulic Plan Design / PFI	LDH	60 days	Wed 9/29/21	Tue 12/28/21	14FF	19						
16	34P-Preliminary Soil Survey	MAT	40 days	Thu 10/28/21	Tue 12/28/21	14FF	19						
17	36C-PFI Constructability Review	PM	14 days	Mon 11/22/21	Mon 12/13/21	14FF-10 days	19						
18	24-Determine Permits Needed	ENV	60 days	Fri 2/26/21	Thu 5/20/21	6	19						
19	36X-PFI Team Meeting Date	PM	1 day	Fri 3/25/22	Fri 3/25/22	13,15,16,17,18,4FF-10 days	33,36						
20	Preliminary Design Phase		307 days	Mon 3/28/22	Fri 6/16/23								
21	25-Draft Environmental Document or CE	ENV	110 days	Mon 4/11/22	Wed 9/14/22	4	52,53						
22	36H-Hydraulic Plan Design / Public Hearing	LDH	75 days	Mon 4/11/22	Tue 7/26/22	4							
23	36P-Plan Design / Public Hearing	LD	130 days	Mon 4/11/22	Wed 10/12/22	4	34,38,35FS-20 days,39						
24	30-Preliminary UFI	LDU	36 days	Mon 4/11/22	Tue 5/31/22	4							
25	32-Value Engineering	PM	60 days	Mon 4/11/22	Tue 7/5/22	4	42						
26	35-Traffic Control Device Recommendations	LDT	60 days	Mon 4/11/22	Tue 7/5/22	4	39						
27	37H-River Mechanics Project Studies	LDH	60 days	Mon 4/11/22	Tue 7/5/22	4	38						
28	37S-Major Structures / Bridge Survey	LDS	85 days	Mon 4/11/22	Tue 8/9/22	4							
29	38-Retaining Wall Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22	4	48						
30	39-Sound Wall Foundation Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22	4	38						
31	40-Minor Structures Data Request	LD	5 days	Mon 4/11/22	Fri 4/15/22	4	33						
32	41-Bridge Foundation Data	MAT	85 days	Mon 3/28/22	Tue 7/26/22	36SS	42						
33	45-Minor Structures Report	MAT	40 days	Mon 4/18/22	Mon 6/13/22	19,31	44						
34	50-Survey Data Verification	LDS	32 days	Thu 10/13/22	Thu 12/1/22	23	39						
35	44-Furnish RWU Data for PHrg/PI Process	RW	20 days	Thu 9/15/22	Wed 10/12/22	23FS-20 days	39						
36	46B-Preliminary Bridge Plans	SB	100 days	Mon 3/28/22	Tue 8/16/22	19	44,32SS						
37	53P-Preliminary Landscaping Plans	LDL	45 days	Mon 4/11/22	Mon 6/13/22	4	55						
38	49C-Design Approval Constructability Review	PM	15 days	Thu 10/13/22	Thu 11/3/22	23,27,30	41						
39	48-Conduct Location/Design Public Hearing	PM	105 days	Fri 12/2/22	Thu 5/4/23	26,34,35,23	41,40FF-14 days						
40	48X-Public Hearing Date	PM	1 day	Fri 4/14/23	Fri 4/14/23	39FF-14 days							
41	49-Adopt Location/Design	LD	30 days	Fri 5/5/23	Fri 6/16/23	39,38	42FF,44,45,46,47,48,49						
42	49X-Location & Design Approval Date	PM	1 day	Fri 6/16/23	Fri 6/16/23	41FF,32,25	52,53						
43	Detailed Design Phase		151 days	Mon 6/19/23	Mon 1/29/24								
44	65F-Plan Design/Field Inspection	LD	150 days	Mon 6/19/23	Fri 1/26/24	33,36,45FF,41	55,54FF-10 days						
45	43H-Hydraulic Plan Design / FI	LDH	85 days	Mon 6/19/23	Wed 10/18/23	41	44FF						
46	46H-Hydrologic / Hydraulic Analysis / Major Structures	LDH	85 days	Mon 6/19/23	Wed 10/18/23	41	55						
47	34F-Furnish Final Soils Survey	MAT	95 days	Mon 6/19/23	Wed 11/1/23	41							
48	54-Retaining Wall Data Report	MAT	32 days	Mon 6/19/23	Wed 8/2/23	29,41	51						
49	55-Noise Abatement Data Report	MAT	32 days	Mon 6/19/23	Wed 8/2/23	41	50						
50	59-Noise Abatement Design	ENV	100 days	Thu 8/3/23	Thu 12/28/23	49							
51	62-Develop Retaining Structure Plans	SB	85 days	Thu 8/3/23	Wed 12/6/23	48							
52	56-Develop Compensatory Mitigation Design	ENV	150 days	Mon 6/19/23	Fri 1/26/24	21,42							
53	56S-Survey Compensatory Mitigation Site	LDS	150 days	Mon 6/19/23	Fri 1/26/24	21,42							
54	65C-FI Constructability Review	PM	15 days	Tue 12/19/23	Wed 1/10/24	44FF-10 days							
55	65X-Field Inspection Team Meeting Date	PM	1 day	Mon 1/29/24	Mon 1/29/24	44,46,37	56FS+40 days						
56	95-District Closeout Completion Date	PIM	210 days	Wed 3/27/24	Wed 1/29/25	55FS+40 days							

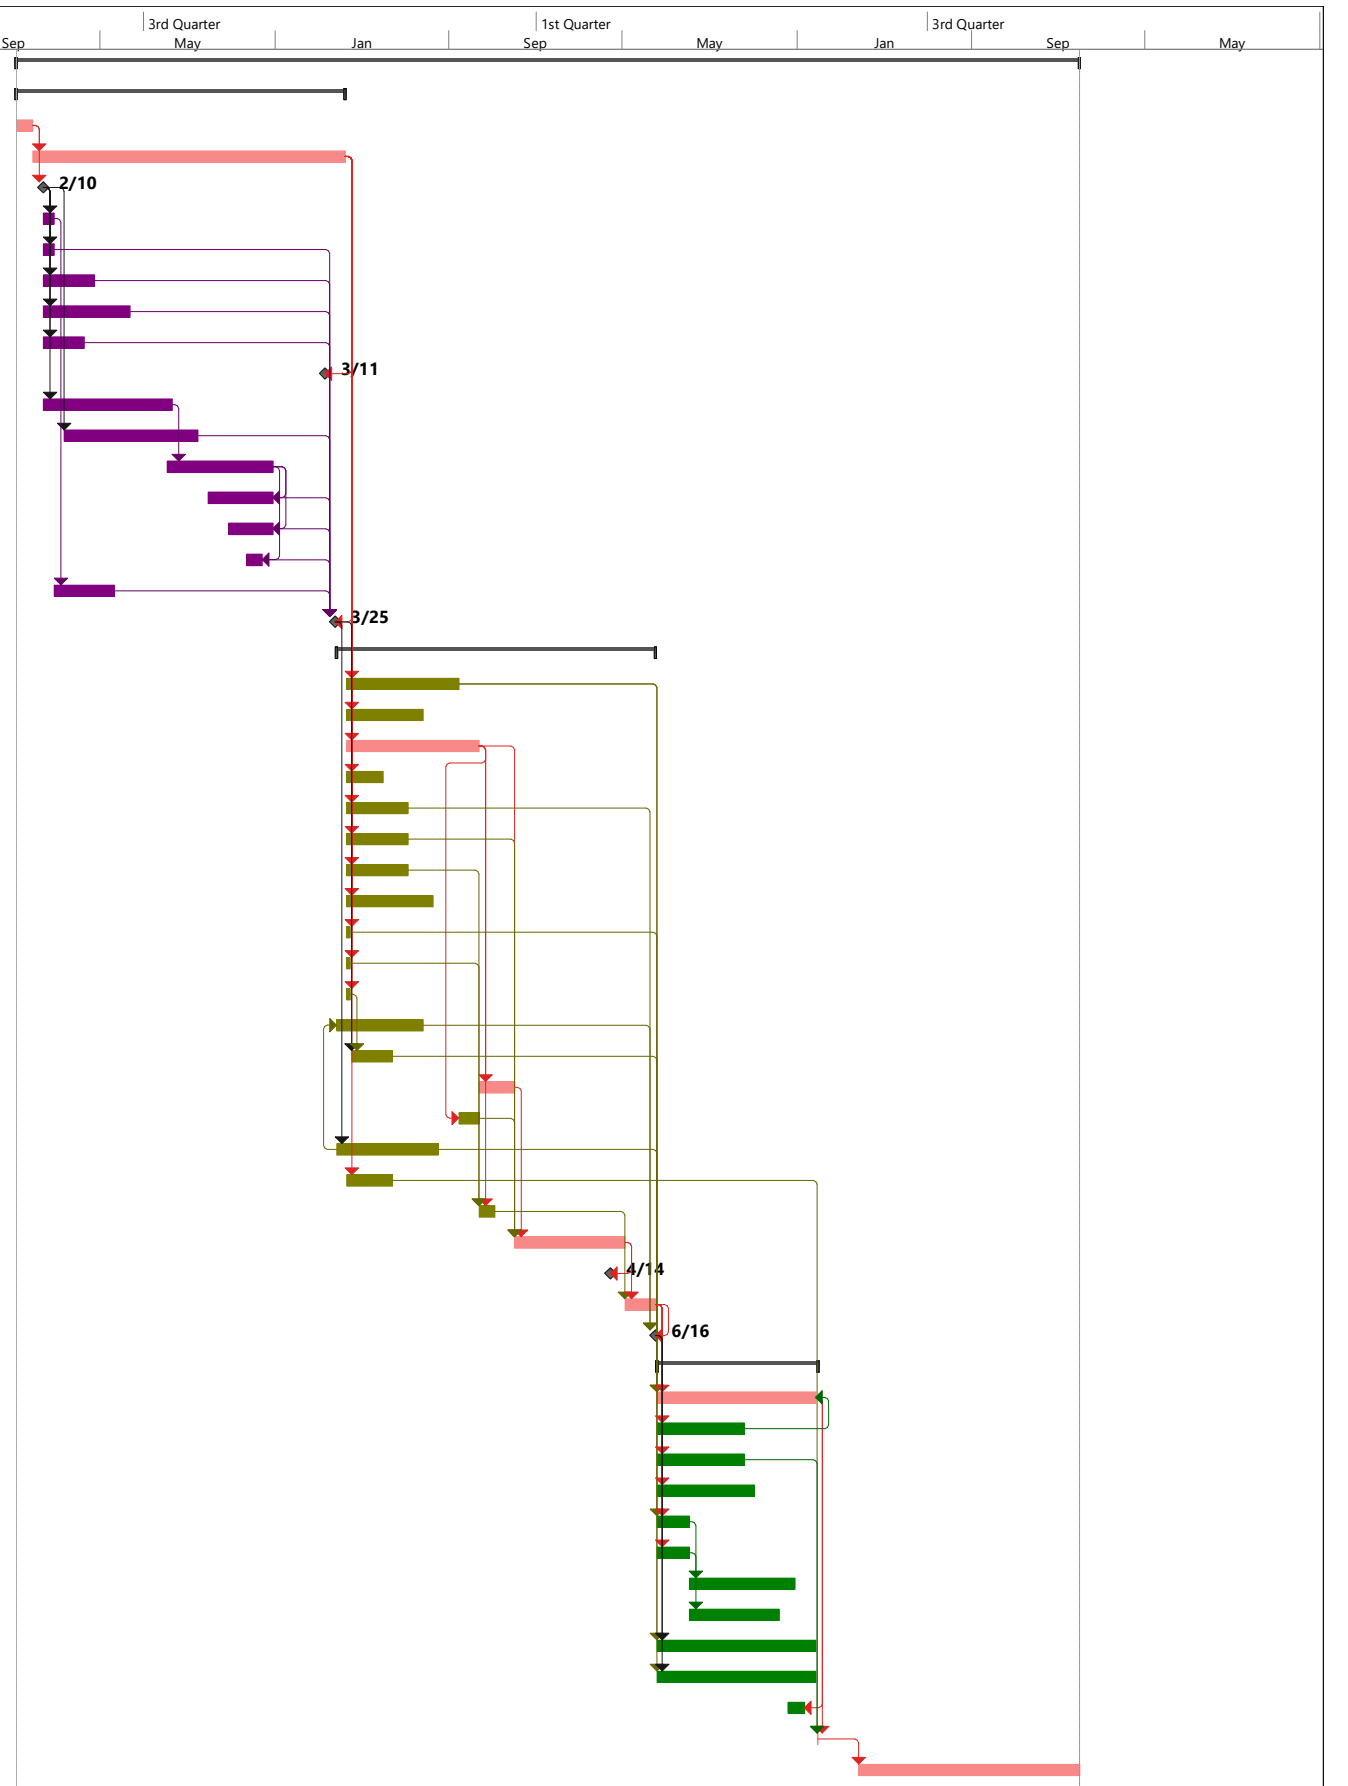

Project: T2_Road_BR_PE
Date: Thu 2/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
