


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	2nd Quarter		3rd Quarter		4th Quarter		1st Quarter	
								Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	PROJECT: Tier 2 - Road work (CN Only)		760 days	Mon 1/4/21	Wed 1/24/24										
2	22-Scope Project	PM	10 days	Mon 1/4/21	Tue 1/19/21		4,6,9								
3	17E-Environmental Review Process (ERP)	ENV	10 days	Mon 1/4/21	Tue 1/19/21										
4	70R-Va Stormwater Mgt Program (VSMP) Const Permit	LDH	40 days	Wed 1/20/21	Wed 3/17/21	2									
5	Advertise Plans Phase		79 days	Wed 1/20/21	Tue 5/11/21										
6	66-Environmental Reevaluation	ENV	20 days	Wed 1/20/21	Tue 2/16/21	2	13								
7	69X-Right of Way / Utility Certification Date	RW	1 day	Tue 5/4/21	Tue 5/4/21	10FF-5 days	13								
8	79-CN Funding Review/Authorization of Funds	PMD	20 days	Wed 1/20/21	Tue 2/16/21	9SS	13								
9	71-Approved CN Plans	PM	52 days	Wed 1/20/21	Fri 4/2/21	2	10SS+16 days,8SS								
10	72-Prepare for Advertisement	CN	63 days	Thu 2/11/21	Tue 5/11/21	9SS+16 days,12FF-11 days,11SS+5 days									
11	72B-Bidability Review	CN	30 days	Thu 2/18/21	Thu 4/1/21	10SS+5 days									
12	72X-Plan Submission Date	CN	1 day	Mon 4/26/21	Mon 4/26/21	10FF-11 days									
13	80-Advertise Project	CN	1 day	Tue 5/11/21	Tue 5/11/21	10FF,8,7,6	15FS+30 days								
14	Construction		641 days	Thu 6/24/21	Wed 1/24/24										
15	82-Conduct Bid Opening	CN	1 day	Thu 6/24/21	Thu 6/24/21	13FS+30 days	16FS+24 days								
16	84-Award Contract	CN	1 day	Fri 7/30/21	Fri 7/30/21	15FS+24 days	17FS+25 days,18FS+25 days								
17	91-Administer Contract	PMC	340 days	Tue 9/7/21	Mon 1/23/23	16FS+25 days	19FS-10 days,20FS+40 days								
18	77S-Construction / Survey	LDS	340 days	Tue 9/7/21	Mon 1/23/23	16FS+25 days									
19	88-Survey Monumentation	LDS	40 days	Fri 1/6/23	Tue 3/7/23	17FS-10 days									
20	95-District Closeout Completion Date	PIM	210 days	Wed 3/22/23	Wed 1/24/24	17FS+40 days									

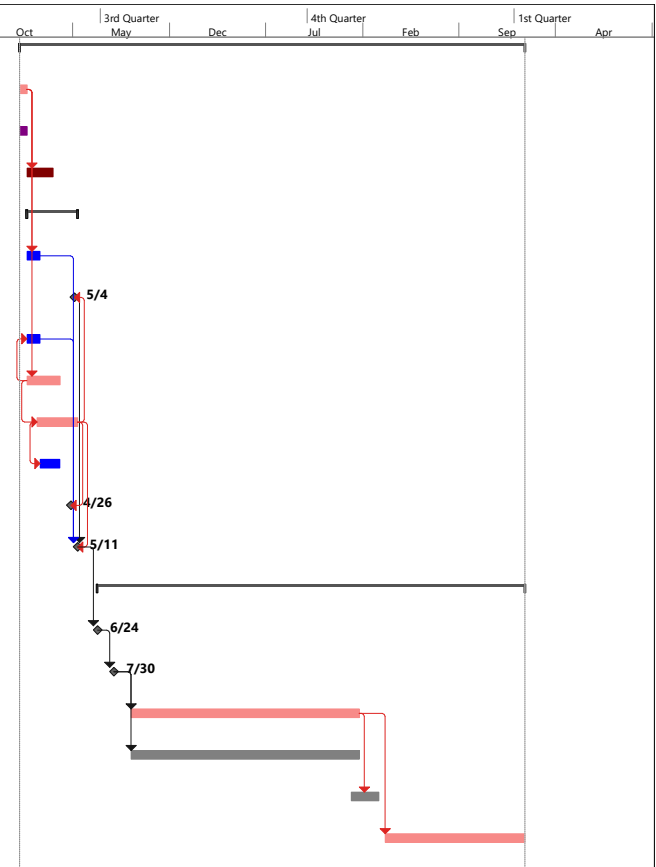

Project: T2_Road_CN
Date: Thu 2/20/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Page 1
