


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	September	July	May	March	January	November
1	PROJECT: LAP Tier 1 PE, CN (WI, On Call)		1116 days	Mon 1/4/21	Wed 6/25/25								
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21		3						
3	12-Authorize Preliminary Engineering	PMD	15 days	Thu 5/13/21	Thu 6/3/21	2	4,5						
4	17E-Environmental Review Process (ERP)	ENV	75 days	Fri 6/4/21	Mon 9/20/21	3	8						
5	28-Consultant Procurement	PM	20 days	Fri 6/4/21	Thu 7/1/21	3	6						
6	22-Scope Project	PM	80 days	Fri 7/2/21	Tue 10/26/21	5	7						
7	65F-Plan Design/Field Inspection	LD	325 days	Wed 10/27/21	Tue 2/21/23	6	10						
8	25-Draft Environmental Document or CE	ENV	85 days	Tue 9/21/21	Thu 1/27/22	4							
9	70-Obtain Environmental Permits	ENV	105 days	Fri 10/21/22	Tue 3/28/23	13FF-60 days							
10	72-Prepare for Advertisement	CN	65 days	Wed 2/22/23	Tue 5/23/23	7	12SS,11SS,13						
11	69X-Right of Way / Utility Certification Date	RW	10 days	Wed 2/22/23	Tue 3/7/23	10SS	13						
12	79-CN Funding Review/Authorization of Funds	PMD	20 days	Wed 2/22/23	Tue 3/21/23	10SS	13						
13	80-Advertise Project	CN	20 days	Wed 5/24/23	Wed 6/21/23	12,11,10	14FS+55 days,9FF-60 days						
14	84-Award Contract	CN	1 day	Mon 9/11/23	Mon 9/11/23	13FS+55 days	15FS+25 days						
15	91-Administer Contract	PMC	170 days	Wed 10/18/23	Mon 6/24/24	14FS+25 days	16FS+40 days						
16	95-District Closeout Completion Date	PIM	210 days	Wed 8/21/24	Wed 6/25/25	15FS+40 days							

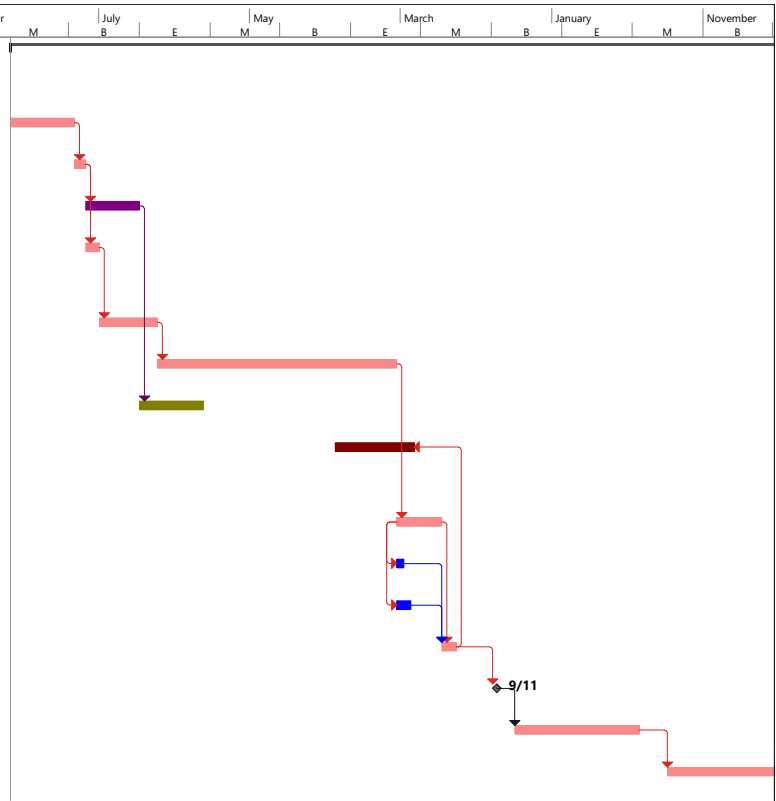

Project: LAP T1\_WI\_OC\_PE\_CN  
Date: Wed 2/12/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
