


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors
1	PROJECT: LAP Tier 1 PE, RW, CN (WI, On Call)		1246 days	Mon 1/4/21	Mon 1/5/26		
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21		3
3	12-Authorize Preliminary Engineering	PMD	15 days	Thu 5/13/21	Thu 6/3/21	2	4,5
4	17E-Environmental Review Process (ERP)	ENV	75 days	Fri 6/4/21	Mon 9/20/21	3	8
5	28-Consultant Procurement	PM	20 days	Fri 6/4/21	Thu 7/1/21	3	6
6	22-Scope Project	PM	80 days	Fri 7/2/21	Tue 10/26/21	5	7
7	65F-Plan Design/Field Inspection	LD	325 days	Wed 10/27/21	Tue 2/21/23	6	9
8	25-Draft Environmental Document or CE	ENV	85 days	Tue 9/21/21	Thu 1/27/22	4	9
9	52-Authorize RW & UT Funds	PMD	25 days	Wed 2/22/23	Tue 3/28/23	7,8	10
10	69-Acquire Right of Way	RW	105 days	Wed 3/29/23	Thu 8/24/23	9	12
11	70-Obtain Environmental Permits	ENV	105 days	Wed 5/3/23	Fri 9/29/23	15FF-60 days	
12	72-Prepare for Advertisement	CN	65 days	Fri 8/25/23	Thu 11/30/23	10	14SS,13SS,15
13	69X-Right of Way / Utility Certification Date	RW	10 days	Fri 8/25/23	Fri 9/8/23	12SS	15
14	79-CN Funding Review/Authorization of Funds	PMD	20 days	Fri 8/25/23	Fri 9/22/23	12SS	15
15	80-Advertise Project	CN	20 days	Fri 12/1/23	Fri 12/29/23	14,13,12 16FS+55 days,11FF-60 days	
16	84-Award Contract	CN	1 day	Fri 3/22/24	Fri 3/22/24	15FS+55 days	17FS+25 days
17	91-Administer Contract	PMC	170 days	Mon 4/29/24	Thu 1/2/25	16FS+25 days	18FS+40 days
18	95-District Closeout Completion Date	PIM	210 days	Wed 3/5/25	Mon 1/5/26	17FS+40 days	

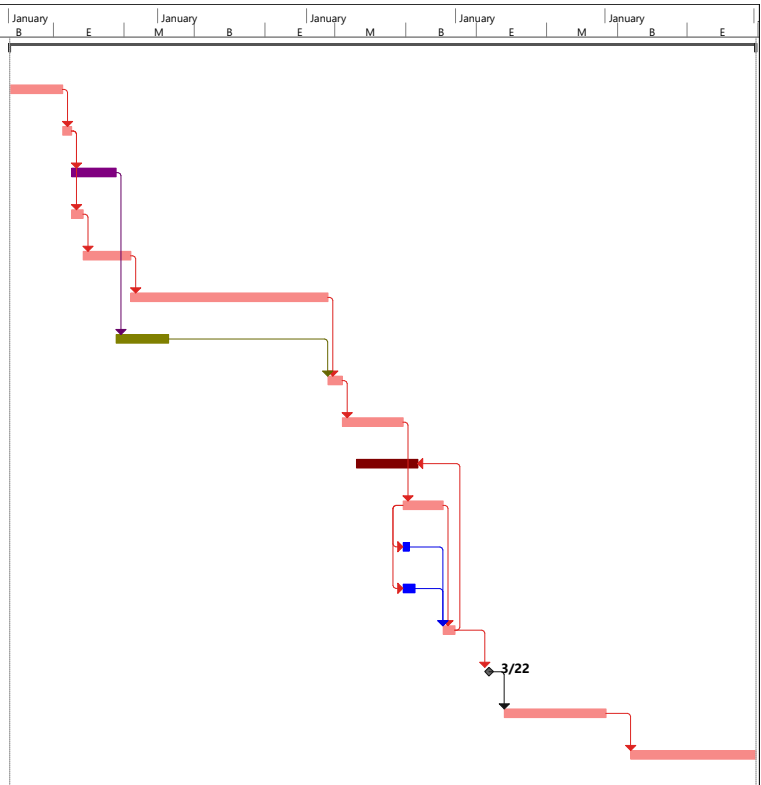

Project: LAP T1\_WI\_OC\_PE\_RW\_C  
Date: Wed 2/12/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
