


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December
1	PROJECT: LAP Tier 2 CN Only		856 days	Mon 1/4/21	Mon 6/10/24																		
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21																		
3	22-Scope Project	PM	10 days	Thu 5/13/21	Wed 5/26/21	2																	
4	70-Obtain Environmental Permits	ENV	110 days	Wed 1/27/21	Thu 7/1/21	8FF-60 days																	
5	72-Prepare for Advertisement	CN	65 days	Thu 5/27/21	Fri 8/27/21	3	755,655,8																
6	69X-Right of Way / Utility Certification Date	RW	10 days	Thu 5/27/21	Thu 6/10/21	5SS																	
7	79-CN Funding Review/Authorization of Funds	PMD	20 days	Thu 5/27/21	Thu 6/24/21	5SS																	
8	80-Advertise Project	CN	20 days	Mon 8/30/21	Mon 9/27/21	7,6,5	9FS+55 days,4FF-60 days																
9	84-Award Contract	CN	1 day	Mon 12/20/21	Mon 12/20/21	8FS+55 days	10FS+25 days																
10	91-Administer Contract	PMC	340 days	Mon 1/31/22	Thu 6/8/23	9FS+25 days	11FS+40 days																
11	95-District Closeout Completion Date	PIM	210 days	Mon 8/7/23	Mon 6/10/24	10FS+40 days																	

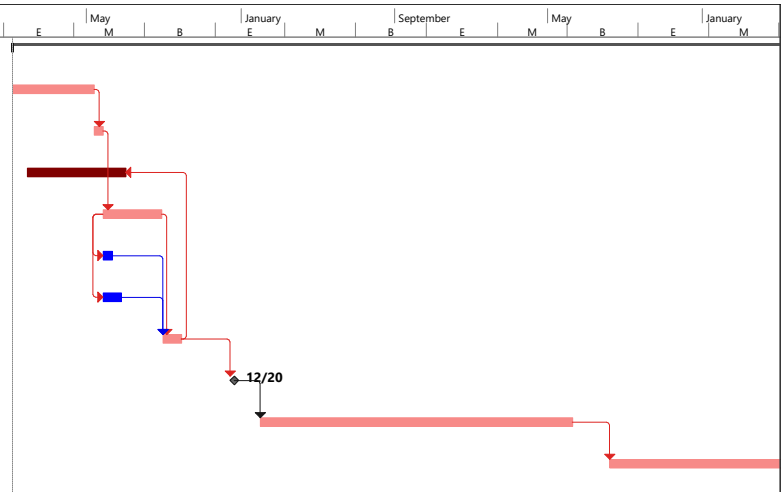

Project: LAP2_CN
Date: Wed 2/12/20

Task	Summary	Inactive Milestone	External Milestone	Duration-only	Start-only	Critical Split
Split	Project Summary	Inactive Summary	Deadline	Manual Summary Rollup	Finish-only	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
