


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors		M	November	E	B	April	M	E	September	B	M	February	E	B	July	M	E	December	B
1	PROJECT: LAP Tier 2 PE,RW,CN (PH,RFP)		1886 days	Mon 1/4/21	Fri 7/28/28																					
2	10-Project Agreement / County / State Agreement	LAD	90 days	Mon 1/4/21	Wed 5/12/21																					
3	12-Authorize Preliminary Engineering	PMD	15 days	Thu 5/13/21	Thu 6/3/21	2																				
4	17E-Environmental Review Process (ERP)	ENV	75 days	Fri 6/4/21	Mon 9/20/21	3																				
5	28-Consultant Procurement	PM	130 days	Fri 6/4/21	Fri 12/10/21	3																				
6	22-Scope Project	PM	170 days	Mon 12/13/21	Tue 8/16/22	5																				
7	65F-Plan Design/Field Inspection	LD	560 days	Wed 8/17/22	Thu 11/14/24	6																				
8	25-Draft Environmental Document or CE	ENV	110 days	Tue 9/21/21	Fri 3/4/22	4																				
9	52-Authorize RW & UT Funds	PMD	25 days	Fri 11/15/24	Mon 12/23/24	7																				
10	69-Acquire Right of Way	RW	140 days	Tue 12/24/24	Wed 7/16/25	9																				
11	70-Obtain Environmental Permits	ENV	170 days	Wed 9/18/24	Tue 5/27/25	15FF-120 days																				
12	72-Prepare for Advertisement	CN	65 days	Thu 7/17/25	Thu 10/16/25	10	14SS,13SS,15																			
13	69X-Right of Way / Utility Certification Date	RW	10 days	Thu 7/17/25	Wed 7/30/25	12SS																				
14	79-CN Funding Review/Authorization of Funds	PMD	20 days	Thu 7/17/25	Wed 8/13/25	12SS																				
15	80-Advertise Project	CN	20 days	Fri 10/17/25	Mon 11/17/25	14,13,12	6FS+55 days,11FF-120 days																			
16	84-Award Contract	CN	1 day	Wed 2/11/26	Wed 2/11/26	15FS+55 days	17FS+25 days																			
17	91-Administer Contract	PMC	340 days	Fri 3/20/26	Wed 7/28/27	16FS+25 days	18FS+40 days																			
18	95-District Closeout Completion Date	PIM	210 days	Fri 9/24/27	Fri 7/28/28	17FS+40 days																				

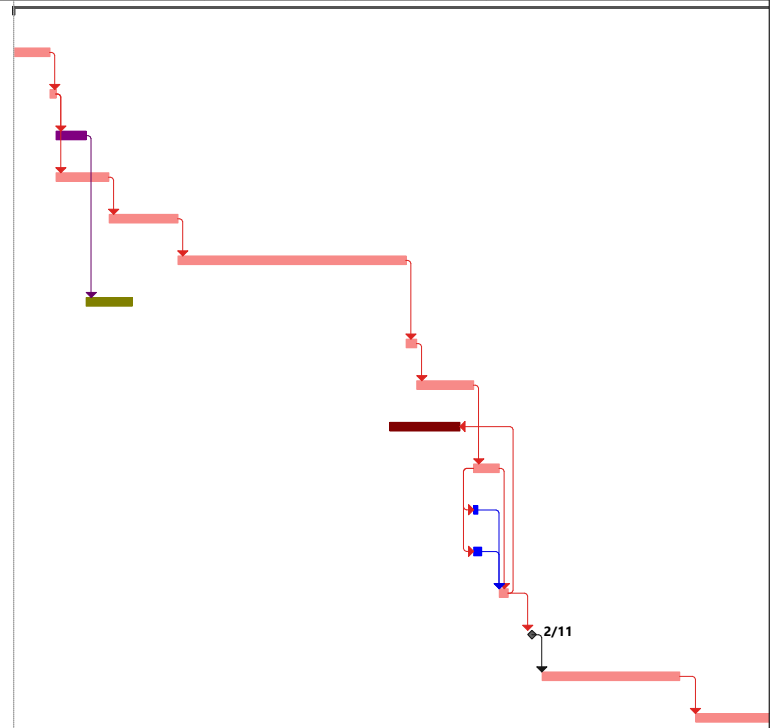

Project: LAP22_PH_RFP_PE_RW_ Date: Wed 2/12/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
