


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	October 9/15	November 3/22	December 9/27	January 4/10	January 17/24	January 31/30	February 11/5	February 12/1
1	PROJECT: Railroad Forces CN Only		716 days	Mon 1/4/21	Wed 11/15/23									
2	68-Clear Railroad Agreements	RW	130 days	Mon 1/4/21	Fri 7/9/21									
3	22-Scope Project	PM	20 days	Mon 7/12/21	Fri 8/6/21	2								
4	17E-Environmental Review Process (ERP)	ENV	10 days	Mon 7/12/21	Fri 7/23/21	3SS								
5	24-Determine Permits Needed	ENV	40 days	Mon 7/26/21	Mon 9/20/21	4								
6	25-Draft Environmental Document or CE	ENV	15 days	Tue 9/21/21	Mon 10/11/21	5								
7	66-Environmental Reevaluation	ENV	5 days	Tue 10/12/21	Tue 10/19/21	6								
8	69X-Right of Way / Utility Certification Date	RW	1 day	Mon 10/4/21	Mon 10/4/21	9FF-10 days								
9	79-CN Funding Review/Authorization of Funds	PMD	20 days	Tue 9/21/21	Tue 10/19/21	3FS+30 days								
10	80-Advertise Project	CN	1 day	Wed 10/20/21	Wed 10/20/21	9								
11	84-Award Contract	CN	15 days	Thu 10/21/21	Wed 11/10/21	10								
12	81-State Forces/Hired Equipment or Railroad Forces	PM	250 days	Fri 11/12/21	Mon 11/14/22	11								
13	95-District Closeout Completion Date	PIM	210 days	Wed 1/18/23	Wed 11/15/23	12FS+40 days								

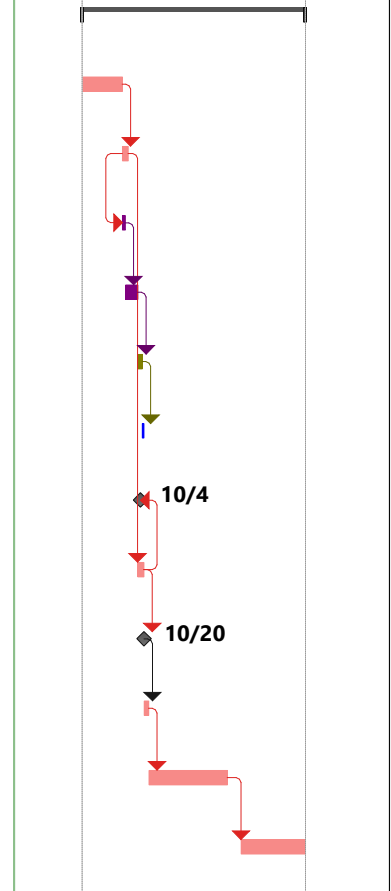

Project: Railroad_Forces_CN Date: Thu 2/20/20	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Progress	
	Milestone		Manual Task		External Tasks		Manual Progress	
	Summary		Duration-only		External Milestone			
	Project Summary		Manual Summary Rollup		Deadline			
	Inactive Task		Manual Summary		Critical			
