


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	September 9/15/21	November 3/22/21	December 9/27/21	January 4/10/21	January 17/23/21	January 30/24/21	February 11/5/21
1	PROJECT: Railroad Forces w PE and CN		731 days	Mon 1/4/21	Fri 12/8/23								
2	68-Clear Railroad Agreements	RW	130 days	Mon 1/4/21	Fri 7/9/21								
3	12-Authorize Preliminary Engineering	PMD	15 days	Mon 7/12/21	Fri 7/30/21	2							
4	22-Scope Project	PM	20 days	Mon 8/2/21	Fri 8/27/21	3							
5	17E-Environmental Review Process (ERP)	ENV	10 days	Mon 8/2/21	Fri 8/13/21	4SS							
6	24-Determine Permits Needed	ENV	40 days	Mon 8/16/21	Mon 10/11/21	5							
7	25-Draft Environmental Document or CE	ENV	15 days	Tue 10/12/21	Tue 11/2/21	6							
8	66-Environmental Reevaluation	ENV	5 days	Wed 11/3/21	Tue 11/9/21	7							
9	69X-Right of Way / Utility Certification Date	RW	1 day	Tue 10/26/21	Tue 10/26/21	10FF-10 days							
10	79-CN Funding Review/Authorization of Funds	PMD	20 days	Tue 10/12/21	Tue 11/9/21	4FS+30 days							
11	80-Advertise Project	CN	1 day	Wed 11/10/21	Wed 11/10/21	10							
12	84-Award Contract	CN	15 days	Fri 11/12/21	Mon 12/6/21	11							
13	81-State Forces/Hired Equipment or Railroad Forces	PM	250 days	Tue 12/7/21	Wed 12/7/22	12							
14	95-District Closeout Completion Date	PIM	210 days	Wed 2/8/23	Fri 12/8/23	13FS+40 days							

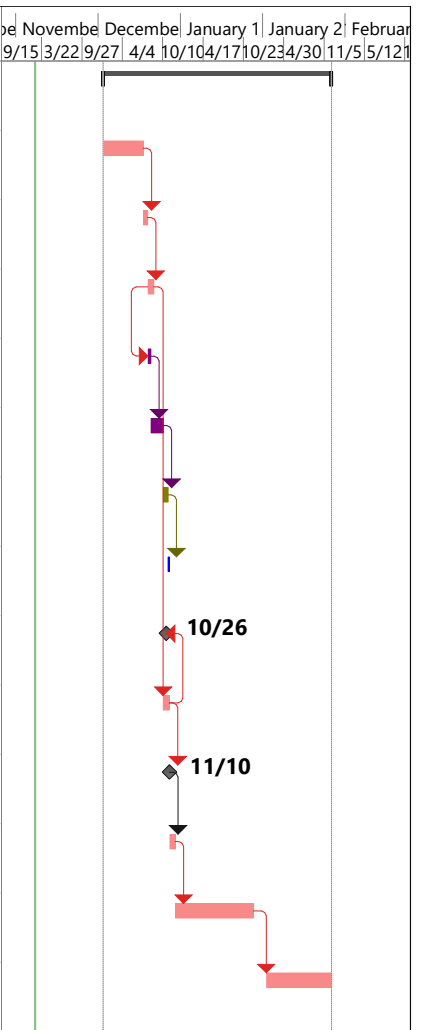

Project: Railroad_Forces_PE_CN Date: Thu 2/20/20	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Progress	
	Milestone		Manual Task		External Tasks		Manual Progress	
	Summary		Duration-only		External Milestone			
	Project Summary		Manual Summary Rollup		Deadline			
	Inactive Task		Manual Summary		Critical			
