


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	June 1 5/17/8/16	December 11/15/2/14	June 21 5/16/8/15	January 1 11/14/2/13	July 1 5/15/8/14
1	PROJECT: Tier 1 - Maintenance (PE Only)		355 days	Mon 1/4/21	Mon 6/6/22						
2	12-Authorize Preliminary Engineering	PMD	10 days	Mon 1/4/21	Tue 1/19/21						
3	22-Scope Project	PM	50 days	Wed 1/20/21	Wed 3/31/21	2					
4	22X-Scoping Team Meeting Date	PM	1 day	Wed 1/27/21	Wed 1/27/21	3SS+5 days					
5	17E-Environmental Review Process (ERP)	ENV	10 days	Thu 4/1/21	Wed 4/14/21	3					
6	24-Determine Permits Needed	ENV	40 days	Thu 4/15/21	Thu 6/10/21	5,8FF					
7	25-Draft Environmental Document or CE	ENV	40 days	Fri 6/11/21	Fri 8/6/21	6,8FF					
8	65F-Plan Design/Field Inspection	LD	40 days	Thu 4/1/21	Wed 5/26/21	3,4					
9	43-Furnish Utility Field Inspection Plans	LD	5 days	Thu 5/27/21	Thu 6/3/21	8					
10	95-District Closeout Completion Date	PIM	210 days	Mon 8/2/21	Mon 6/6/22	9FS+40 days					

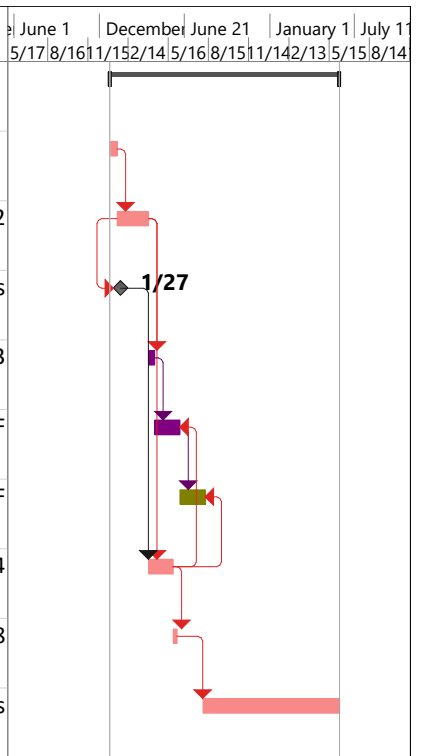

Project: T1_Maint_All_PE Date: Thu 2/20/20	Task		Inactive Milestone		Start-only		Critical Split	
	Split		Inactive Summary		Finish-only		Progress	
	Milestone		Manual Task		External Tasks		Manual Progress	
	Summary		Duration-only		External Milestone			
	Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical				
