


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	r	Apr	Sep	1st Quarter	Feb	Jul	1st Quarter	Dec	May	1st Quarter	Oct	Mar	Aug
1	PROJECT: Tier 1 - Road work (CN Only)		570 days	Mon 1/4/21	Tue 4/18/23															
2	22-Scope Project	PM	10 days	Mon 1/4/21	Tue 1/19/21			7,10												
3	17E-Environmental Review Process (ERP)	ENV	14 days	Mon 1/4/21	Mon 1/25/21															
4	70-Obtain Environmental Permits	ENV	105 days	Mon 1/4/21	Thu 6/3/21	14FF-60 days														
5	70R-Va Stormwater Mgt Program (VSMP) Const Permit	LDH	40 days	Mon 1/4/21	Wed 3/3/21															
6	Advertise Plans Phase		59 days	Wed 1/20/21	Tue 4/13/21															
7	66-Environmental Reevaluation	ENV	10 days	Wed 1/20/21	Tue 2/2/21	2		14												
8	69X-Right of Way / Utility Certification Date	RW	1 day	Thu 3/25/21	Thu 3/25/21	11FF-5 days		14												
9	79-CN Funding Review/Authorization of Funds	PMD	20 days	Wed 1/20/21	Tue 2/16/21	10SS		14												
10	71-Approved CN Plans	PM	27 days	Wed 1/20/21	Fri 2/26/21	2		14												
11	72-Prepare for Advertisement	CN	35 days	Thu 2/11/21	Thu 4/1/21	10SS+16 days,13FF-11 days,12SS+5 days														
12	72B-Bidability Review	CN	5 days	Thu 2/18/21	Thu 2/25/21	11SS+5 days														
13	72X-Plan Submission Date	CN	1 day	Wed 3/17/21	Wed 3/17/21	11FF-11 days														
14	80-Advertise Project	CN	1 day	Tue 4/13/21	Tue 4/13/21	11FF,9,8,7														
15	Construction		471 days	Wed 5/26/21	Tue 4/18/23															
16	82-Conduct Bid Opening	CN	1 day	Wed 5/26/21	Wed 5/26/21	14FS+30 days														
17	84-Award Contract	CN	1 day	Thu 7/1/21	Thu 7/1/21	16FS+24 days														
18	91-Administer Contract	PMC	170 days	Mon 8/9/21	Fri 4/15/22	17FS+25 days														
19	77S-Construction / Survey	LDS	170 days	Mon 8/9/21	Fri 4/15/22	17FS+25 days														
20	88-Survey Monumentation	LDS	40 days	Mon 4/4/22	Fri 5/27/22	18FS-10 days														
21	95-District Closeout Completion Date	PIM	210 days	Tue 6/14/22	Tue 4/18/23	18FS+40 days														

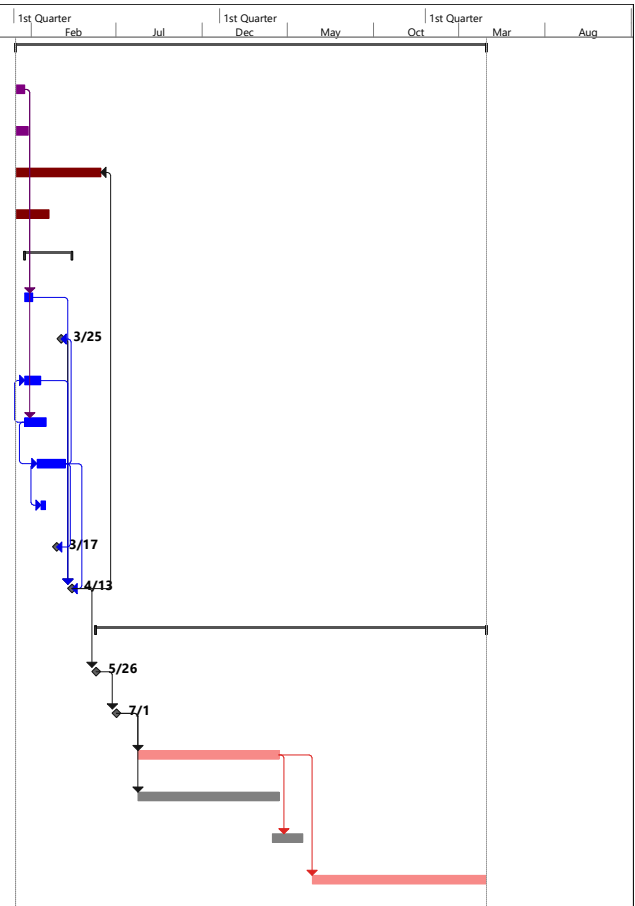

Project: T1_Road_CN
Date: Thu 2/20/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Page 1
