


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	2nd Quarter	3rd Quarter	4th Quarter	1st Quarter				
								Mar	Oct	May	Dec	Jul	Feb	Sep	Apr
1	PROJECT: Tier 1 - Road work (RW & CN Only)		806 days	Mon 1/4/21	Fri 3/29/24										
2	22-Scope Project	PM	10 days	Mon 1/4/21	Tue 1/19/21		5,7								
3	17E-Environmental Review Process (ERP)	ENV	14 days	Mon 1/4/21	Mon 1/25/21										
4	Final Design and ROW Acquisition Phase		220 days	Wed 1/20/21	Fri 12/3/21										
5	43-Furnish Utility Field Inspection Plans	LD	30 days	Wed 1/20/21	Wed 3/3/21		2, 6SS+15 days								
6	43X-Utility Field Inspection Team Meeting Date	PM	1 day	Wed 2/10/21	Wed 2/10/21		5SS+15 days								
7	58-Survey Right of Way Plan Sheets	LDS	35 days	Wed 1/20/21	Wed 3/10/21		2								
8	51-Furnish R/W and Utility Plans	LD	45 days	Thu 3/11/21	Wed 5/12/21		6,7								
9	51X-Right of Way and Utilities Plan Date	PM	1 day	Thu 5/13/21	Thu 5/13/21		8								
10	52-Authorize RW & UT Funds	PMD	25 days	Thu 5/13/21	Thu 6/17/21		9SS								
11	52X-Right of Way and Utilities Authorization Date	PMD	1 day	Thu 6/17/21	Thu 6/17/21		10FF								
12	57S-Right of Way Survey & Stakeout	LDS	65 days	Fri 6/18/21	Mon 9/20/21		11								
13	60P-NTP for Partial RW Acquisitions	RW	10 days	Fri 6/18/21	Thu 7/1/21		10								
14	60X-Final RW and Utilities Notice to Proceed Date	RW	1 day	Fri 7/2/21	Fri 7/2/21		11,13								
15	69-Acquire Right of Way	RW	105 days	Fri 7/2/21	Fri 12/3/21		13								
16	73-Process Relocations	RW	90 days	Fri 7/2/21	Tue 11/9/21		13								
17	65P-Plan Design (PAC)	LD	85 days	Fri 6/25/21	Tue 10/26/21		18,8								
18	51H-Hydraulic Review for Construction / PAC	LDH	30 days	Thu 5/13/21	Thu 6/24/21		8								
19	61-Final Traffic Control Device Plans	LDT	85 days	Fri 6/25/21	Tue 10/26/21		17SS								
20	46-Review & Approval of ESC and SWM Plan	LDH	10 days	Fri 11/12/21	Mon 11/29/21		22								
21	71C-PAC Constructability Review	PM	10 days	Wed 10/27/21	Tue 11/9/21		17,19								
22	71X-PreAdvertisement Conference (PAC) Date	PM	1 day	Wed 11/10/21	Wed 11/10/21		12,14,16,17,18,24,21								
23	70-Obtain Environmental Permits	ENV	105 days	Mon 7/26/21	Mon 12/27/21		36FF-60 days								
24	67-Clear Utility Agreements	RW	85 days	Fri 7/2/21	Tue 11/2/21		13,26FS-11 days,25FS-11 days								
25	67U-Utility Relocation By Others	RW	85 days	Wed 11/17/21	Thu 3/24/22		24FS-11 days,15FS-11 days								
26	70S-Utility Stakeout / Survey	LDS	85 days	Wed 11/17/21	Thu 3/24/22		24FS-11 days,15FS-11 days								
27	70R-Va Stormwater Mgt Program (VSMP) Const Permit	LDH	40 days	Wed 11/10/21	Tue 1/11/22		22SS								
28	Advertise Plans Phase		89 days	Fri 11/12/21	Fri 3/25/22										
29	66-Environmental Reevaluation	ENV	10 days	Fri 11/12/21	Mon 11/29/21		22								
30	69X-Right of Way / Utility Certification Date	RW	1 day	Mon 1/24/22	Mon 1/24/22		33FF-5 days								
31	79-CN Funding Review/Authorization of Funds	PMD	20 days	Fri 11/12/21	Mon 12/13/21		32SS								
32	71-Approved CN Plans	PM	27 days	Fri 11/12/21	Wed 12/22/21		22								
33	72-Prepare for Advertisement	CN	35 days	Wed 12/8/21	Mon 1/31/22		32SS+16 days,35FF-11 days,34SS+5 days								
34	72B-Bidability Review	CN	5 days	Wed 12/15/21	Tue 12/21/21		33SS+5 days								
35	72X-Plan Submission Date	CN	1 day	Wed 1/12/22	Wed 1/12/22		33FF-11 days								
36	80-Advertise Project	CN	1 day	Fri 3/25/22	Fri 3/25/22		33FF,31,30,29,25								
37	Construction		471 days	Mon 5/9/22	Fri 3/29/24										
38	82-Conduct Bid Opening	CN	1 day	Mon 5/9/22	Mon 5/9/22		36FS+30 days								
39	84-Award Contract	CN	1 day	Tue 6/14/22	Tue 6/14/22		38FS+24 days								
40	91-Administer Contract	PMC	170 days	Thu 7/21/22	Wed 3/29/23		39FS+25 days								
41	77S-Construction / Survey	LDS	170 days	Thu 7/21/22	Wed 3/29/23		39FS+25 days								
42	88-Survey Monumentation	LDS	40 days	Thu 3/16/23	Wed 5/10/23		40FS-10 days								
43	95-District Closeout Completion Date	PIM	210 days	Thu 5/25/23	Fri 3/29/24		40FS+40 days								

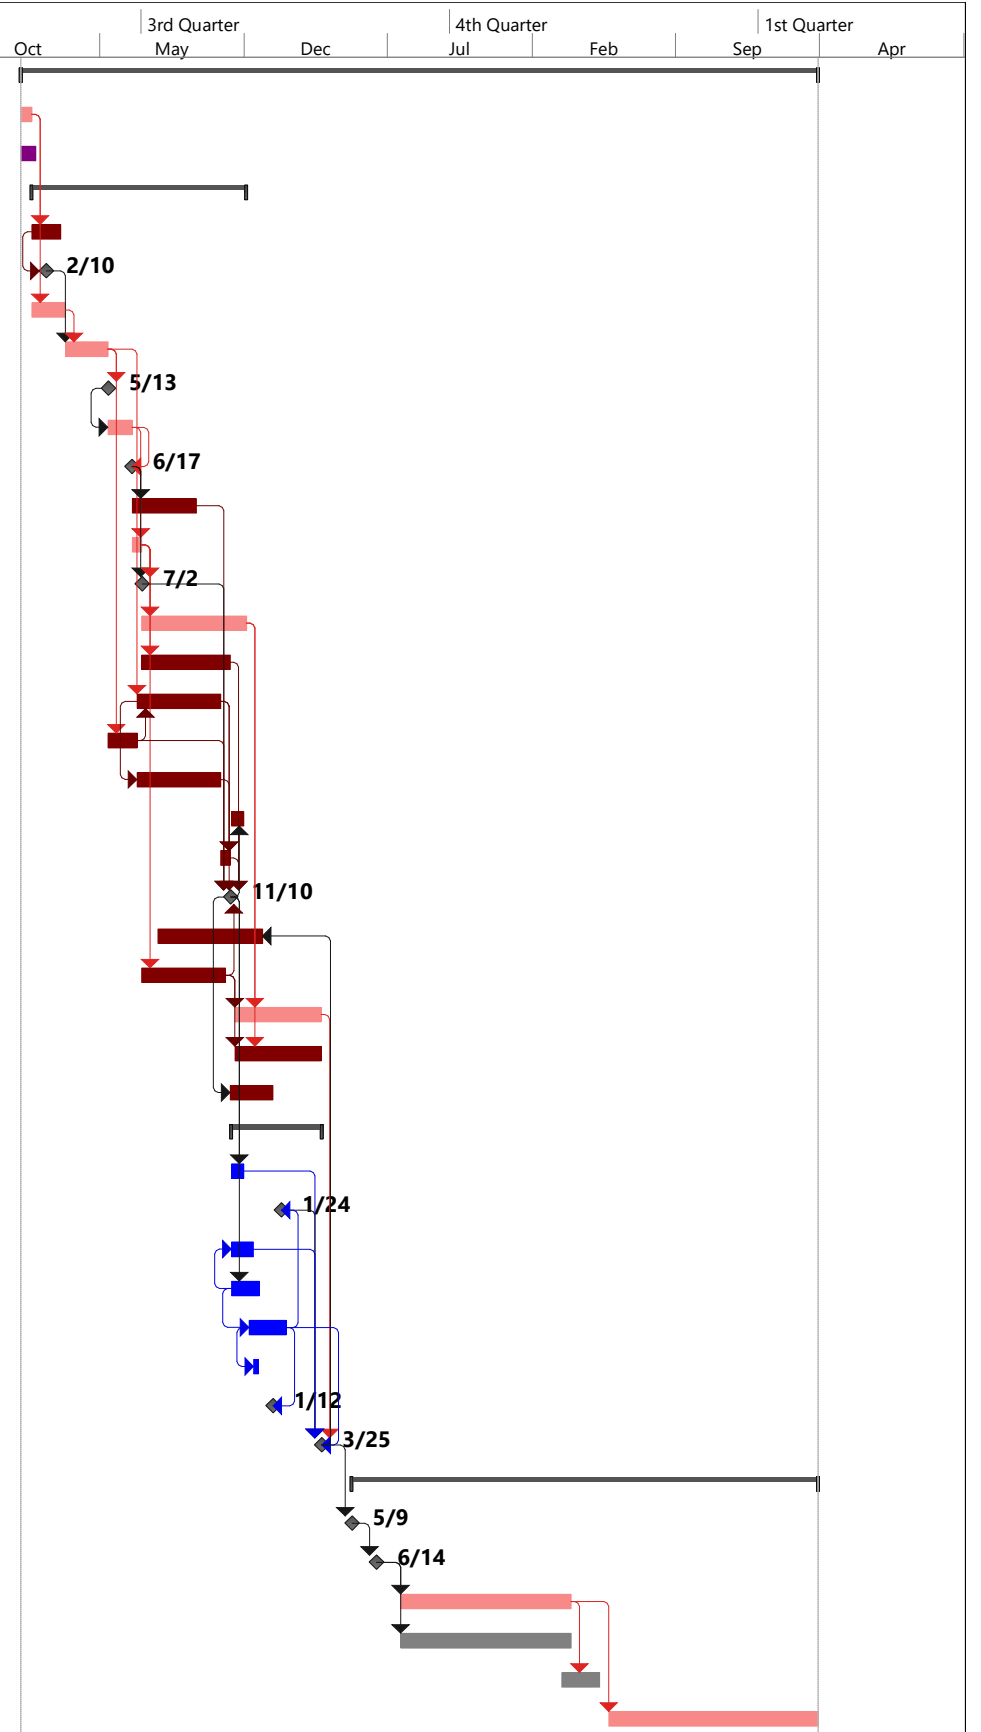

Project: T1_Road_UT_RW_CN Date: Thu 2/20/20	Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
