


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors											
1	<b>PROJECT: State forces/Hired equip w RW and CN</b>		<b>537 days</b>	<b>Mon 1/4/21</b>	<b>Thu 3/2/23</b>													
2	<b>22-Scope Project</b>	PM	20 days	Mon 1/4/21	Tue 2/2/21		3SS+1 day,5											
3	<b>17E-Environmental Review Process (ERP)</b>	ENV	10 days	Tue 1/5/21	Wed 1/20/21		2SS+1 day	4										
4	<b>24-Determine Permits Needed</b>	ENV	15 days	Thu 1/21/21	Wed 2/10/21	3		11										
5	<b>65F-Plan Design/Field Inspection</b>	LD	40 days	Wed 2/3/21	Wed 3/31/21	2		6,8										
6	<b>52-Authorize RW &amp; UT Funds</b>	PMD	10 days	Thu 4/1/21	Wed 4/14/21	5		7										
7	<b>69-Acquire Right of Way</b>	RW	130 days	Thu 4/15/21	Tue 10/19/21	6	8FF,10FF,9FF,12											
8	<b>70R-Va Stormwater Mgt Program (VSMP) Const P</b>	LDH	40 days	Mon 8/23/21	Tue 10/19/21	7FF,5		13										
9	<b>46-Review &amp; Approval of ESC and SWM Plan</b>	LDH	10 days	Tue 10/5/21	Tue 10/19/21	7FF												
10	<b>79-CN Funding Review/Authorization of Funds</b>	PMD	10 days	Tue 10/5/21	Tue 10/19/21	7FF		13										
11	<b>66-Environmental Reevaluation</b>	ENV	5 days	Thu 2/11/21	Wed 2/17/21	4		13										
12	<b>69X-Right of Way / Utility Certification Date</b>	RW	1 day	Wed 10/20/21	Wed 10/20/21	7		13										
13	<b>80-Advertise Project</b>	CN	1 day	Thu 10/21/21	Thu 10/21/21	10,8,12,11		14										
14	<b>81-State Forces/Hired Equipment or Railroad Forc</b>	PM	85 days	Fri 10/22/21	Tue 3/1/22	13	15FS+40 days											
15	<b>95-District Closeout Completion Date</b>	PIM	210 days	Wed 4/27/22	Thu 3/2/23	14FS+40 days												

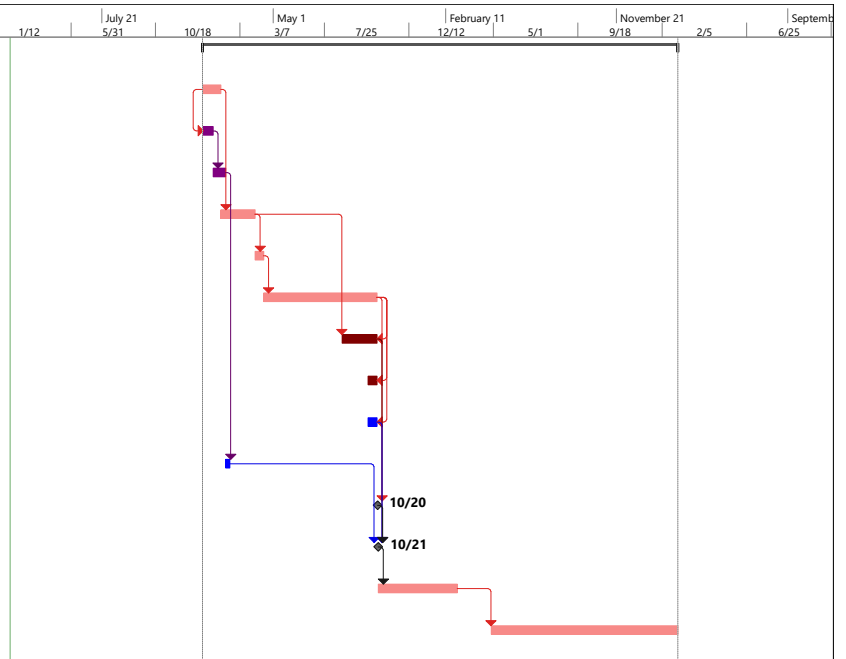

Project: T1\_State\_Force\_Hired\_E  
Date: Thu 2/20/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Page 1
