


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors	Timeline (3/8 to 12/11)											
1	PROJECT: Tier 1 and 2 - Right of Way Only		416 days	Mon 1/4/21	Wed 8/31/22			[Timeline bar from 1/4/21 to 8/31/22]											
2	17E-Environmental Review Process (ERP)	ENV	5 days	Mon 1/4/21	Fri 1/8/21			[Timeline bar from 1/4/21 to 1/8/21]											
3	Final Design and ROW Acquisition Phase		416 days	Mon 1/4/21	Wed 8/31/22			[Timeline bar from 1/4/21 to 8/31/22]											
4	52-Authorize RW & UT Funds	PMD	25 days	Mon 1/4/21	Tue 2/9/21		5	[Timeline bar from 1/4/21 to 2/9/21]											
5	60X-Final RW and Utilities Notice to Proceed Date	RW	1 day	Wed 2/10/21	Wed 2/10/21	4	6	[Timeline bar at 2/10/21]											
6	69-Acquire Right of Way	RW	140 days	Thu 2/11/21	Mon 8/30/21		5, 7FS+40 days	[Timeline bar from 2/11/21 to 8/30/21]											
7	95-District Closeout Completion Date	PIM	210 days	Thu 10/28/21	Wed 8/31/22		6FS+40 days	[Timeline bar from 10/28/21 to 8/31/22]											

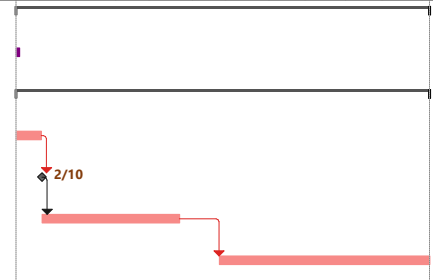

Project: T1_T2_RW
Date: Thu 2/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
