


ID	Task Name	Responsible Division	Duration	Start	Finish	Predecessors	Successors
1	PROJECT: Task Order PE and CN		404 days	Mon 1/4/21	Mon 8/15/22		
2	12-Authorize Preliminary Engineering	PMD	15 days	Mon 1/4/21	Tue 1/26/21		3,4
3	22-Scope Project	PM	70 days	Wed 1/27/21	Wed 5/5/21	2	9
4	17E-Environmental Review Process (ERP)	ENV	5 days	Wed 1/27/21	Tue 2/2/21	2	5,6
5	24-Determine Permits Needed	ENV	10 days	Wed 2/3/21	Tue 2/16/21	4	6
6	25-Draft Environmental Document or CE	ENV	20 days	Wed 2/17/21	Wed 3/17/21	4,5	7,11
7	47-Approve Willingness	PM	3 days	Thu 3/18/21	Mon 3/22/21	6	8
8	65F-Plan Design/Field Inspection	LD	40 days	Tue 3/23/21	Mon 5/17/21	7	9
9	49-Adopt Location/Design	LD	10 days	Tue 5/18/21	Tue 6/1/21	8,3	10,12
10	69X-Right of Way / Utility Certification Date	RW	1 day	Wed 6/2/21	Wed 6/2/21	9	12
11	66-Environmental Reevaluation	ENV	5 days	Thu 3/18/21	Wed 3/24/21	6	13
12	79-CN Funding Review/Authorization of Funds	PMD	10 days	Thu 6/3/21	Wed 6/16/21	10,9	13
13	80-Advertise Project	CN	5 days	Thu 6/17/21	Wed 6/23/21	12,11	14
14	84-Award Contract	CN	5 days	Thu 6/24/21	Wed 6/30/21	13	15
15	91-Administer Contract	PMC	130 days	Thu 7/1/21	Mon 1/10/22	14	16FS+40 days
16	95-District Closeout Completion Date	PIM	110 days	Fri 3/11/22	Mon 8/15/22	15FS+40 days	

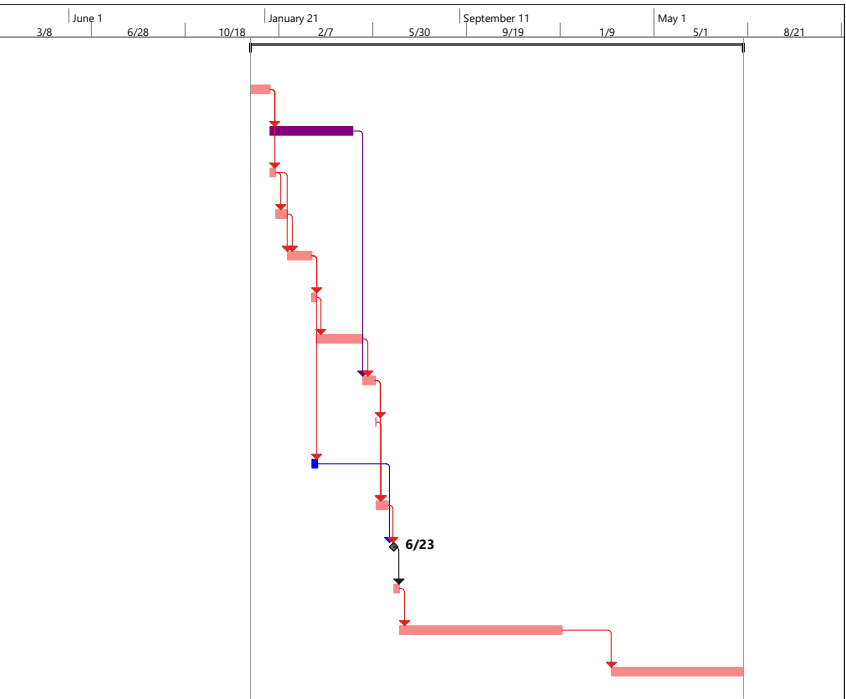

Project: Task_Order_PE_CN
Date: Thu 2/20/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Page 1
